



SURFACE IMPOUNDMENT CLOSURE PLAN

Bremo Power Station – West and East Ash Ponds

Permit #618

Submitted to:



Bremo Power Station

1038 Bremo Road
Bremo Bluff, VA 23022

Submitted by:

Golder Associates Inc.

2108 West Laburnum Ave, Suite 200,
Richmond, Virginia 23227
804 358-7900

Project # 152-0347

May 11, 2018
Revised September 2018

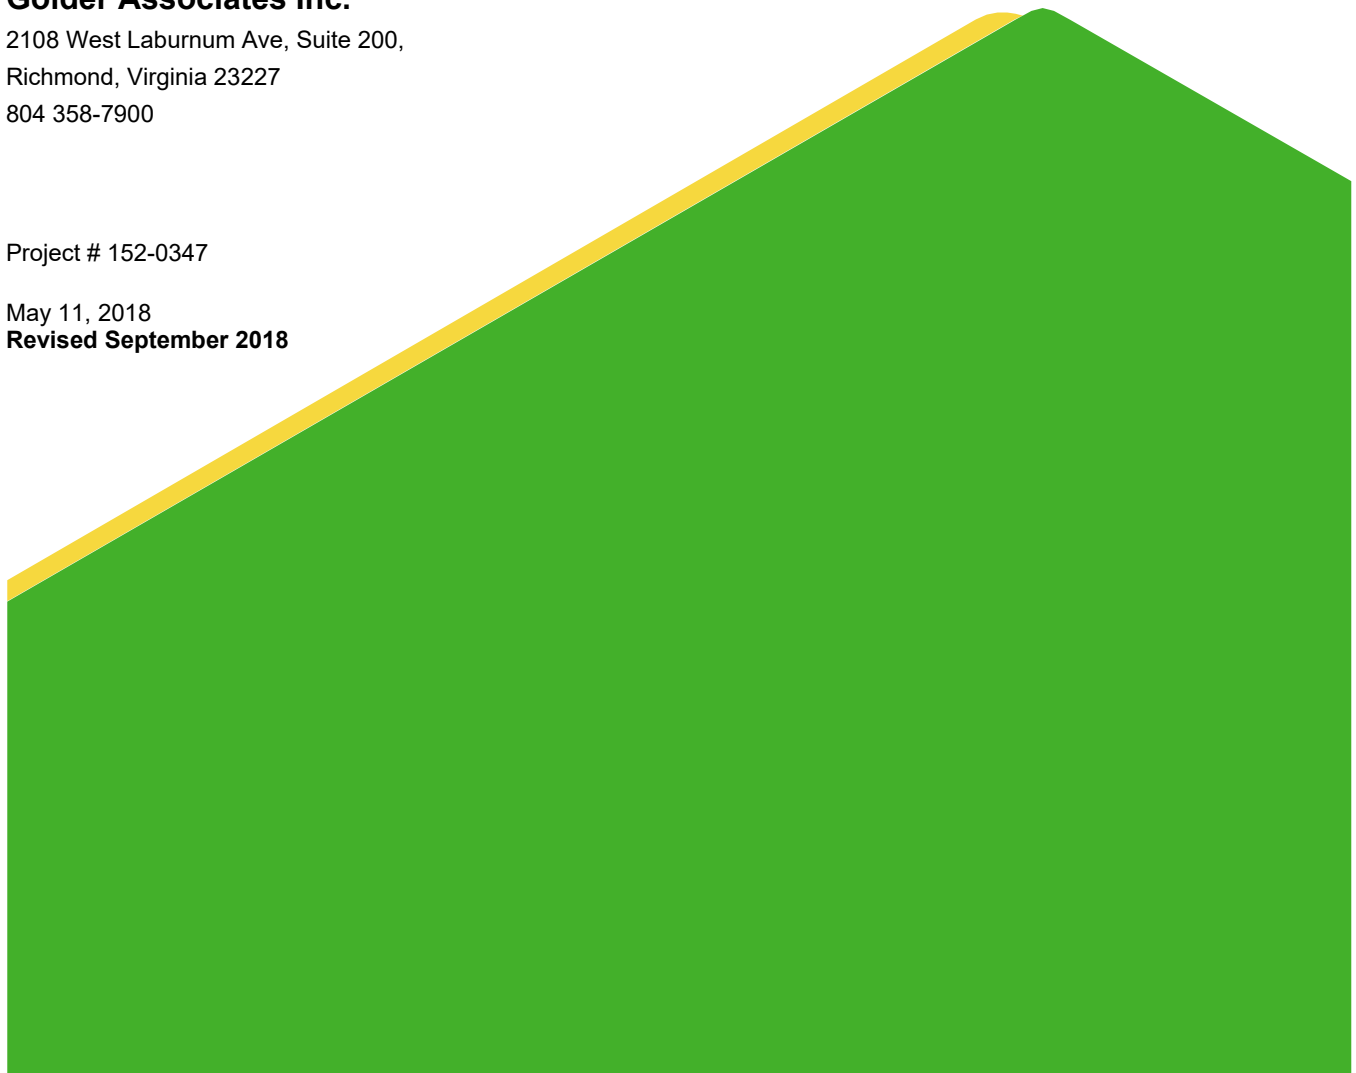


Table of Contents

1.0	PLAN CERTIFICATION	1
2.0	INTRODUCTION.....	2
2.1	General Impoundment Information	2
2.1.1	West Ash Pond.....	2
2.1.2	East Ash Pond.....	2
3.0	CLOSURE IMPLEMENTATION.....	3
3.1	Overview of Closure Approach	3
4.0	CLOSURE TIMEFRAMES	3
5.0	INVENTORY REMOVAL AND DISPOSAL.....	4
5.1	Waste Removal, Decontamination and Disposal.....	4
5.2	Sampling and Testing Program.....	4
5.3	Other Areas	5
6.0	CLOSURE OF SUPPORT PONDS AND BASINS.....	5
7.0	CLOSURE IMPLEMENTATION.....	5
7.1	Posting	5
7.2	Certification	5
7.3	Post-Closure Uses	6
8.0	CLOSURE COST ESTIMATE.....	6

Tables

Table 1	Closure Schedule
---------	------------------

Attachments

Attachment 1	Closure by Removal Drawings
Attachment 2	Closure Cost Estimate


1.0 PLAN CERTIFICATION

This Closure Plan for the Bremo Power Station's West Ash Pond (WAP) and East Ash Pond (EAP) was prepared by Golder Associates Inc. (Golder). The document and Certification/Statement of Professional Opinion are based on and limited to information that Golder has relied on from Dominion Energy and others, but not independently verified, as well as work products produced by Golder.

On the basis of and subject to the foregoing, it is my professional opinion as a Professional Engineer licensed in the Commonwealth of Virginia that this document has been prepared in accordance with good and accepted engineering practices as exercised by other engineers practicing in the same discipline(s), under similar circumstances, at the same time, and in the same locale. It is my professional opinion that the document was prepared consistent with the requirements in §257.102 of the United States Environmental Protection Agency's "Standards for the Disposal of Coal Combustion Residuals in Landfills and Surface Impoundments," published in the Federal Register on April 17, 2015, with an effective date of October 19, 2015 (40 CFR §257.102), as well as with the requirements in §257.100 resulting from the EPA's "Hazardous and Solid Waste Management System: Disposal of Coal Combustion Residuals From Electric Utilities; Extension of Compliance Deadlines for Certain Inactive Surface Impoundments; Response to Partial Vacatur" published in the Federal Register on August 5, 2016 with an effective date of October 4, 2016 (40 CFR §257.100).

The use of the word "certification" and/or "certify" in this document shall be interpreted and construed as a Statement of Professional Opinion, and is not and shall not be interpreted or construed as a guarantee, warranty, or legal opinion.

Ron DiFrancesco, P. E.
Printed Name of Professional Engineer



025260
Commonwealth of Virginia License No.

Signature and Date

2.0 INTRODUCTION

This Closure Plan (Plan) was prepared for the Bremo Power Station's (Station) inactive Coal Combustion Residuals (CCR) surface impoundments, the West Ash Pond (WAP) and East Ash Pond (EAP). This Closure Plan was prepared in accordance with 40 CFR Part §257, Subpart D and is consistent with the requirements of 40 CFR §257.102 for closure of CCR surface impoundments, 40 CFR §257.100(e)(6)(i), and Virginia Solid Waste Management Regulations 9 VAC20-81-800. The Station, owned and operated by Virginia Electric and Power Company d/b/a Dominion Energy Virginia (Dominion), is located in Bremo Bluff, Virginia at 1038 Bremo Road, north of the James River.

The WAP and EAP are being closed as CCR surface impoundments under the CCR rule provisions at 40 CFR §257. The ponds will be closed by removal of CCR pursuant to 40 CFR §257.102(c). All elevations noted in this document, unless stated otherwise, are in feet relative to the North American Vertical Datum of 1988 (NAVD-88).

2.1 General Impoundment Information

2.1.1 West Ash Pond

The WAP is approximately 17 acres in size and was used as a water treatment pond to settle and manage low-volume wastewaters, including CCR. In 2014, the Station converted from a coal-fired power plant to a natural gas-fired power plant. No new CCR has been placed in the WAP after the conversion. The WAP contained approximately 327,000 cubic yards (CY) of CCR prior to the start of excavation activities.

The WAP is regulated under the following permits:

- Virginia Department of Environmental Quality (DEQ) Virginia Pollutant Discharge Elimination System (VPDES) Permit No. VA0004138
- DEQ VPDES Construction General Permit No. VAR10H875
- Virginia Department of Conservation and Recreation (DCR) Operation and Maintenance Certificate, Inventory No. 06511

2.1.2 East Ash Pond

The EAP is an approximately 26.5-acre impoundment that was used for the storage of CCR from the Bremo Power Station. The pond was placed into service in the 1930's and was capped with soil fill in the mid-1980's except for the eastern portion of the pond, which remained wet, allowing pass-through of drainage from the adjacent area to the north. The EAP contained approximately 1,800,000 cubic yards (CY) of CCR prior to the start of excavation activities.

The EAP is regulated under the following permits:

- Virginia Department of Environmental Quality (DEQ) Virginia Pollutant Discharge Elimination System (VPDES) Permit No. VA0004138
- DEQ VPDES Construction General Permit No. VAR10H875
- Virginia Department of Conservation and Recreation (DCR) Operation and Maintenance Certificate, Inventory No. 00815

3.0 CLOSURE IMPLEMENTATION

3.1 Overview of Closure Approach

This plan provides for the closure of the WAP and EAP by removal of the CCR material. Closure is considered complete under 40 CFR 257.102 and 9 VAC20-81-810 when:

1. A Professional Engineer licensed in the Commonwealth of Virginia certifies all CCR has been removed from the units followed by an over-excavation of approximately 6 inches of soil.
2. The unit's downgradient groundwater monitoring wells do not exhibit levels in excess of a maximum contaminant limit (MCL) or established groundwater protection standard for any CCR Appendix IV constituent *after a minimum of ten sampling events have occurred after CCR material has been verified as removed by a professional engineer licensed in Virginia.*

At the time of writing, the majority of CCR in the ponds has been relocated to the North Ash Pond (NAP). Final CCR removal will either be consolidated in the NAP, or disposed of in a designated off-site facility. After completing the removal of CCR from the WAP, the embankments will be stabilized and/or removed and the remaining former pond area will be re-graded and left as a grassy open area. After completing the removal of CCR from the EAP, the embankments will be stabilized and the area will be repurposed as the East Stormwater Management Pond. In addition, a discrete area of fugitive CCR has been identified along the southern portion of the EAP embankment. This area will be further characterized and the residual CCR will be removed as part of the EAP closure.

During and after closure, the existing network of groundwater monitoring wells will be sampled and tested to determine the monitored constituent concentrations required in 40 CFR §257 Appendix IV.

4.0 CLOSURE TIMEFRAMES

Table 1 below outlines the estimated sequence of scheduled closure activities.

Table 1: Closure Schedule

Activity	Tentative Date
Completion of CCR Removal	By October 2018
Completion of Closure Construction	By January 2019
Certification of Construction Completion	By April 2019

Closure is considered complete when the elements of this Closure Plan specified above have been performed, as certified by a Professional Engineer licensed in the Commonwealth of Virginia. This certification will be included as part of a closure certification report. In accordance with 40 CFR §257.102(h), Dominion will prepare a notification of closure of the CCR unit within 30 days of completion of closure, and place the notification in the operating record.

5.0 INVENTORY REMOVAL AND DISPOSAL

5.1 Waste Removal, Decontamination and Disposal

The protocol for closure by removal of materials within the EAP and WAP will involve removing accumulated CCR such that no residual materials remain visible, followed by over-excavating the removal footprint by approximately 6 inches. Removed CCR and CCR-mixed soil will either be consolidated in the NAP or taken to an off-site disposal facility. To facilitate stormwater management, construction, and/or structural stabilization of embankments or excavations, closure by removal of areas within the ponds may be achieved in phases. Phased closures may be sequenced as necessary to support traffic patterns, stormwater controls, etc.

Material removal against embankments may involve excavation of the upstream embankment face to a near-vertical condition. Immediately after excavation and inspection of these areas for certification, fill soil will be placed and compacted against the embankment to re-establish stable slopes of no steeper than 2 horizontal to 1 vertical (2H:1V). For rock, existing concrete designated to remain, or other similar hard surfaces (e.g. pipes or foundation supports to remain), the surface will be cleaned to a visually-clean condition through mechanical means such as pressure washing. The soils surrounding said hard areas will be removed to the 6-inch over-excavation criterion. After CCR removal and certification, the WAP will be graded to drain. Vegetative stabilization will be established to prevent erosion. The area will be maintained as a grassy open area. After CCR removal and certification in the EAP, the pond subgrade will be shaped and modifications will be made to the existing outlet structure. Vegetative stabilization will be established to prevent erosion.

5.2 Sampling and Testing Program

After removal of the 6-inch over-excavation material, the area will be visually inspected to verify the CCR and over-excavation has been achieved. The ponds will be further inspected by targeted soil cores for visual inspection to a depth of at least 6 inches at a frequency of at least one core per acre. The soil cores will be dug by hand, using a hand auger or similar tool, and be a minimum of 6-inches deep.

Verification surveys of the pond closure will be prepared by a Commonwealth of Virginia-licensed Land Surveyor and will consist of a survey of the “visually clean” surface and a survey of the “over-excavation”

surface to verify the minimum 6-inch removal. Certification of the closure by removal will be provided by a Commonwealth of Virginia-licensed Professional Engineer.

Groundwater monitoring will be conducted in accordance with the approved Groundwater Monitoring Plan to meet the closure by removal standard set forth in 40 CFR 257.102(c) and the Virginia Solid Waste Management Regulations.

5.3 Other Areas

During the evaluation of the nature and extent of CCRs in and around the EAP, a thin area of residual CCR material was identified along a portion of the toe of the East Pond embankment. Additional permits from the Corps of Engineers and Fluvanna County may be required to authorize removal of materials in this area, and Dominion will obtain all necessary permits prior to performing removal activities in this area. The identified materials will be removed to a visually clean condition and relocated to the North Pond. Verification and documentation of the removal will be provided by a Virginia-licensed Professional Engineer. After removal and verification, the vegetation in the area will be restored with equivalent vegetation as per the applicable permits.

6.0 CLOSURE OF SUPPORT PONDS AND BASINS

There are no supporting ponds or basins associated with the WAP or EAP.

7.0 CLOSURE IMPLEMENTATION

7.1 Posting

One sign will be posted at the site entrance to each pond notifying all persons of the final closure and prohibition against further receipt of CCR. Unauthorized access to the site will be controlled by natural barriers or lockable gates across the access roads.

7.2 Certification

Upon completion of closure construction, a certification statement signed by a licensed Professional Engineer will be placed in the operating record and submitted to the DEQ along with the documentation from the Sampling and Testing Program. The certification statement shall read as follows:

I certify that closure has been completed in accordance with the Closure Plan dated [DATE] for solid waste permit number 618 issued to Dominion, with the exception of the following discrepancies: [To Be Determined]

In addition, a sign(s) was (were) posted on [DATE] at the site entrance notifying all persons of the closing [and state other notification procedures if applicable] and

barriers [indicate type] were installed at [location] to prevent new waste from being deposited.

[Signature, date and stamp of Professional Engineer]

7.3 Post-Closure Uses

No post-closure use of the WAP area is proposed. The EAP will be repurposed as the East Stormwater Management Pond for stormwater and low volume wastewaters from the Station.

8.0 CLOSURE COST ESTIMATE

The closure cost estimate for the WAP and EAP is \$18,041,661. This estimated amount covers the remaining excavation, inspection, testing, and certification as proposed in this Plan.

DOMINION ENERGY

BREMO POWER STATION


CLOSURE BY REMOVAL PLAN

WEST ASH POND & EAST ASH POND

SOLID WASTE PERMIT No. 618


FLUVANNA COUNTY, VIRGINIA

SEPTEMBER 2018

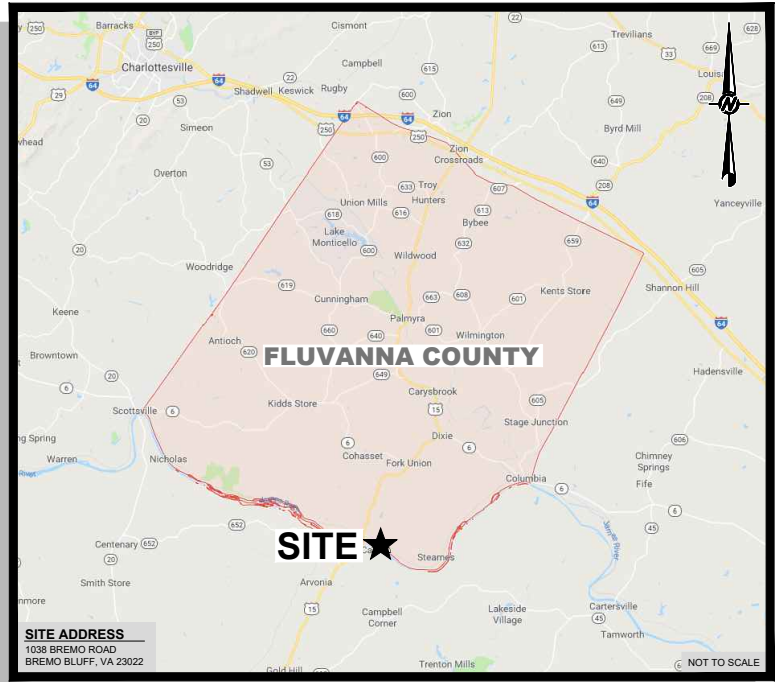

VICINITY MAP

DRAWING INDEX	
DRAWING No.	DRAWING TITLE
CBR-1	COVER SHEET
CBR-2	WEST ASH POND PRE-CLOSURE TOPOGRAPHY (APPROXIMATE BOTTOM OF POND)
CBR-3	WEST ASH POND CLOSURE BY REMOVAL PLAN
CBR-4	WEST ASH POND CONCEPTUAL FINAL GRADING PLAN
CBR-5	WEST ASH POND CROSS-SECTIONS
CBR-6	EAST ASH POND PRE-CLOSURE TOPOGRAPHY (APPROXIMATE BOTTOM OF POND)
CBR-7	EAST ASH POND CLOSURE BY REMOVAL PLAN
CBR-8	EAST ASH POND CONCEPTUAL FINAL GRADING PLAN
CBR-9	EAST ASH POND CROSS-SECTIONS

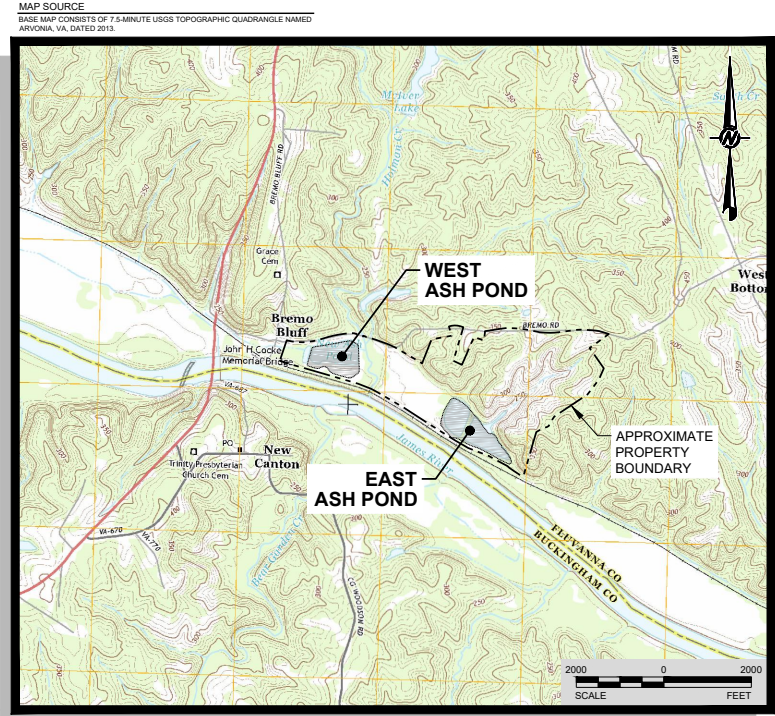

SITE LOCATION MAP

PREPARED BY:



GOLDER ASSOCIATES, INC.
MAIN CONTACT: RON DiFRANCESCO, P.E.
2108 W. LABURNUM AVE., SUITE 200
RICHMOND, VIRGINIA 23227
PHONE: (804) 358-7900
EMAIL: RON_DiFRANCESCO@GOLDER.COM

PREPARED FOR:



DOMINION ENERGY
MAIN CONTACT: MIKE GLAGOLA
5000 DOMINION BOULEVARD
GLEN ALLEN, VIRGINIA 23060
PHONE: (804) 273-4547
EMAIL: MICHAEL.A.GLAGOLA@DOMINIONENERGY.COM

REV.	MMDDYY	DESCRIPTION	DESIGN	CADD	CHECK	REVIEW
1	09/14/18	RESPONSE TO DEQ TR COMMENTS	JRD	BPG	DPM	JRD
0	05/07/18	ISSUED FOR PERMIT	JRD	BPG	DPM	JRD




CLIENT
DOMINION ENERGY
BREMO POWER STATION
FLUVANNA COUNTY, VIRGINIA

CONSULTANT
GOLDER ASSOCIATES, INC.
2108 WEST LABURNUM AVENUE
SUITE 200
RICHMOND, VA 23227
(804) 358-7900
www.golder.com

GOLDER

PROJECT CLOSURE BY REMOVAL PLAN WEST ASH POND & EAST ASH POND SOLID WASTE PERMIT No. 618	TITLE COVER SHEET	PROJECT NO. 15-20347	DRAWING CBR-1
---	-----------------------------	-------------------------	-------------------------

Path: G:\Plan Production Data Files\Drawing Data Files\15-20347\DWG - EAP and WAP Closure by Removal\Active Drawings\1520347D0A.MXD.dwg

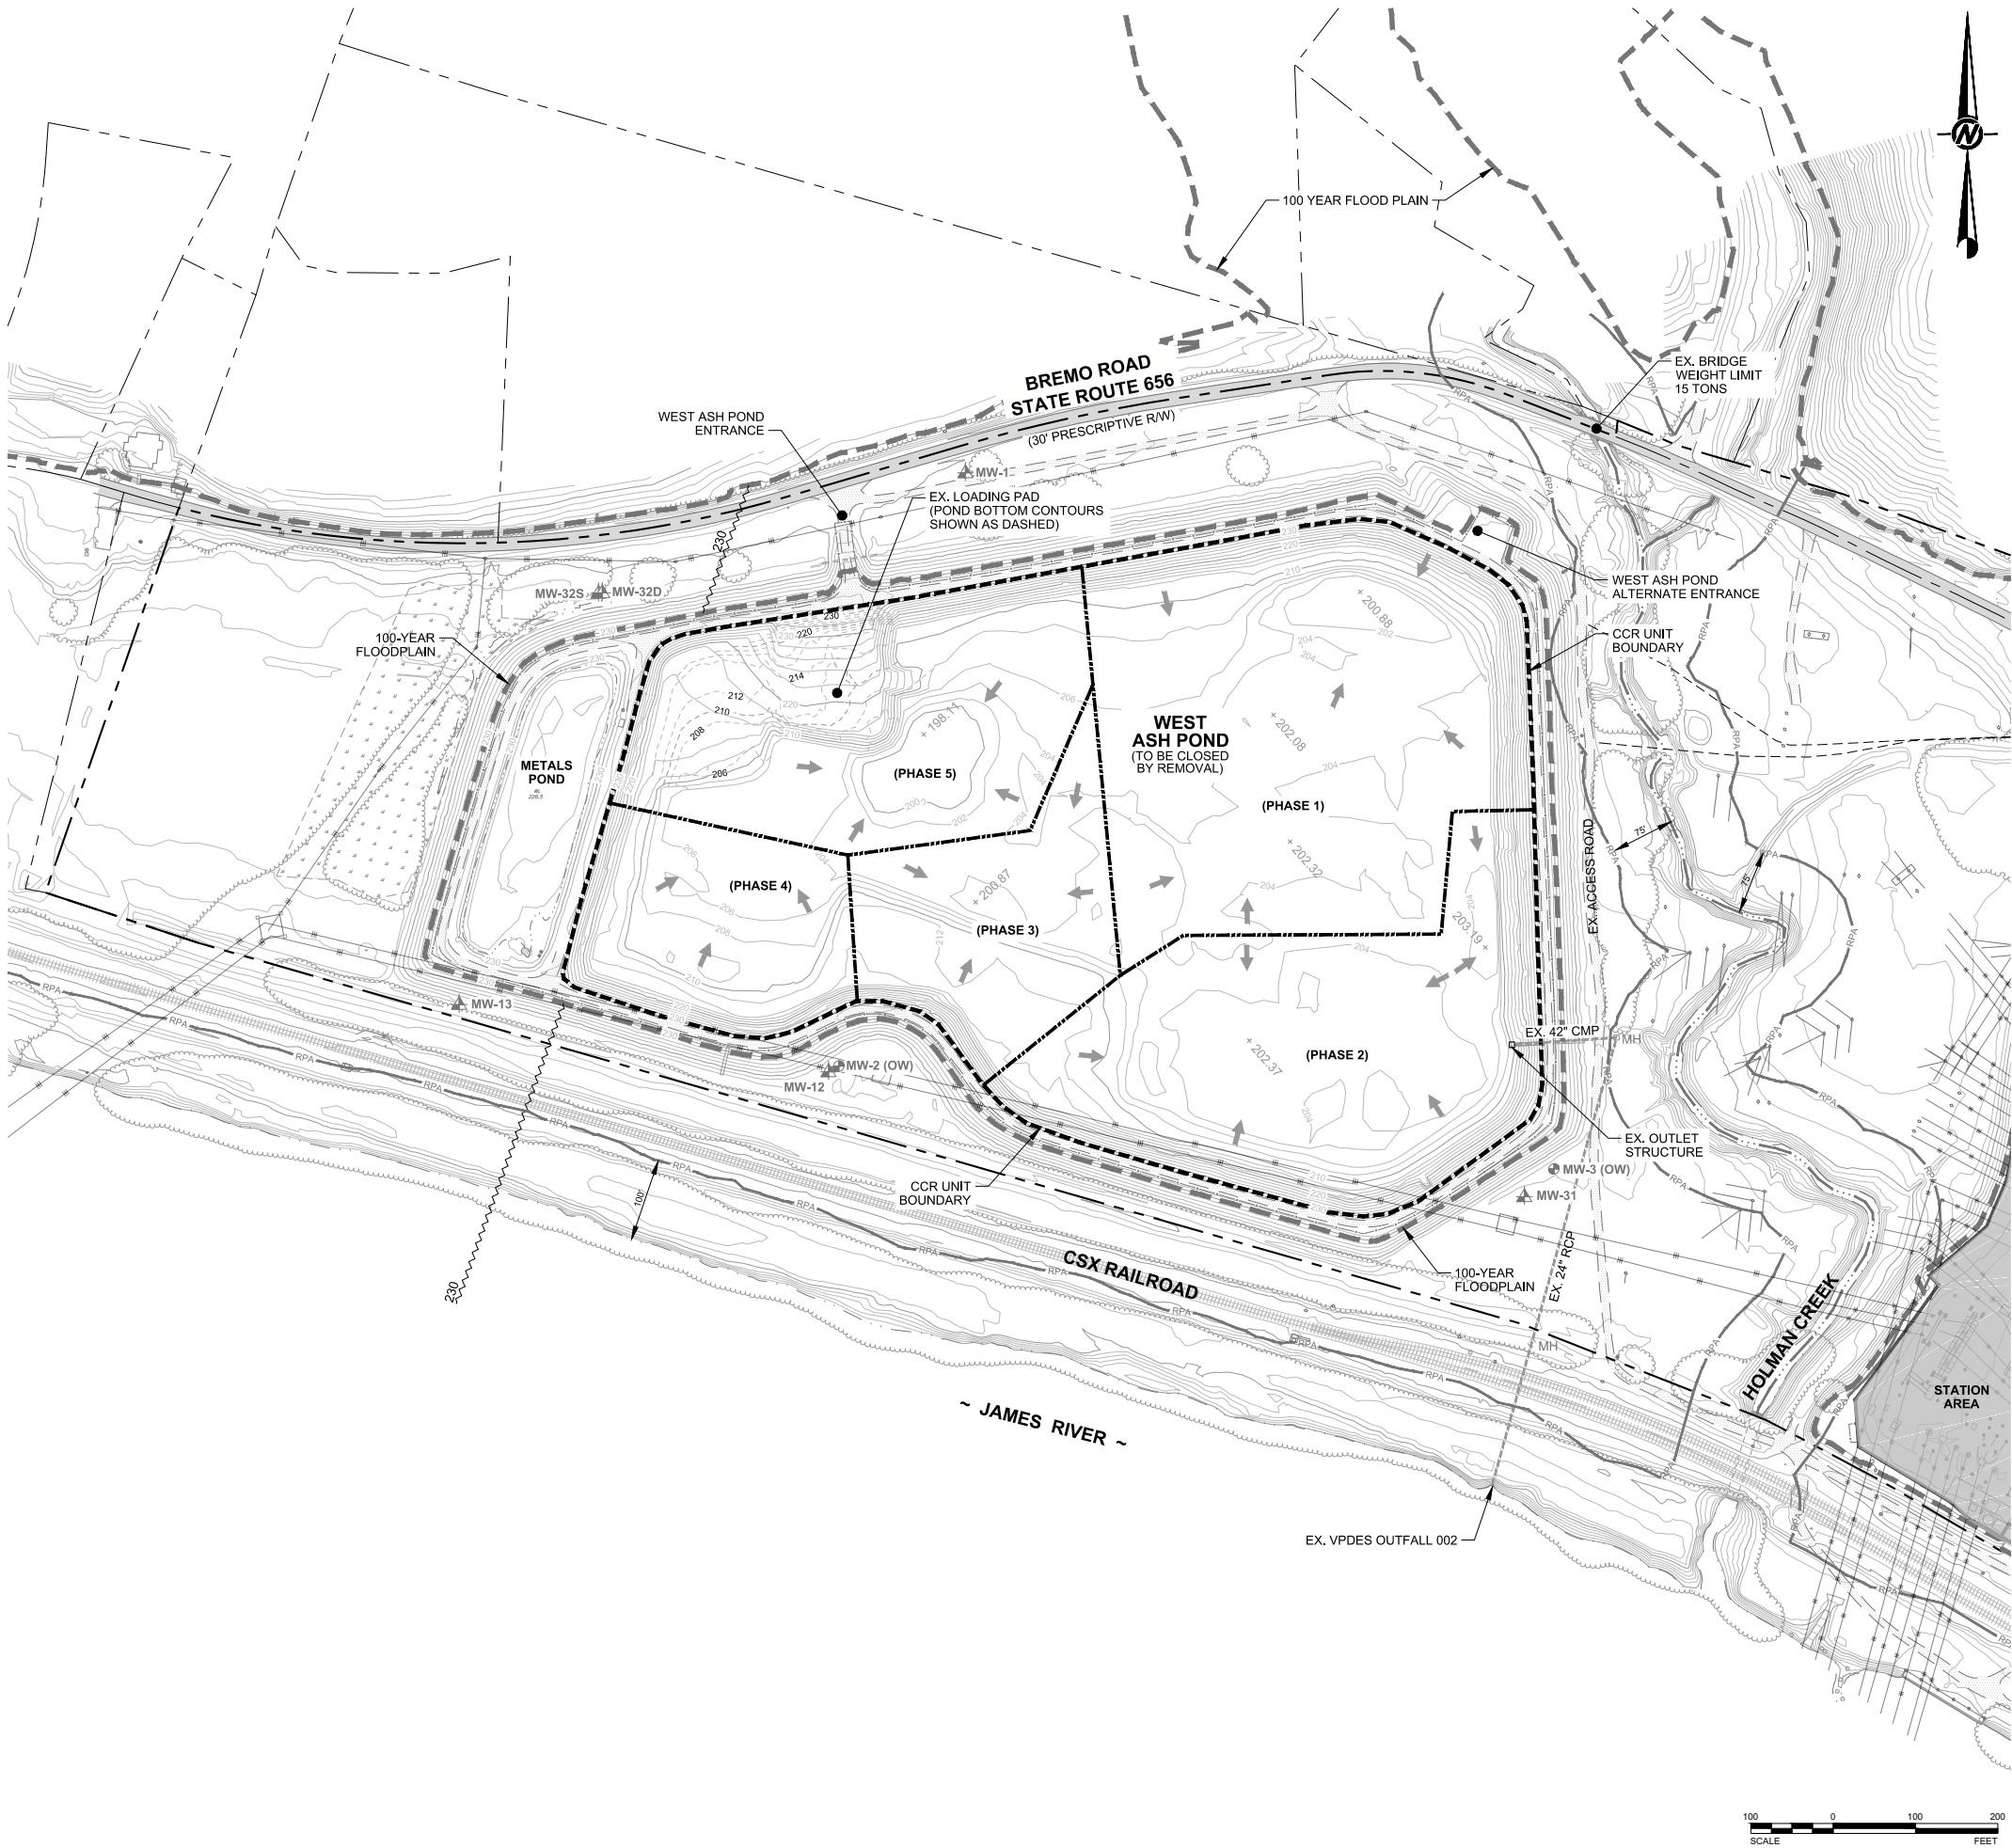

LEGEND	
	DOMINION PROPERTY BOUNDARY
	ADJACENT PROPERTY BOUNDARY
	CCR UNIT BOUNDARY
	EXISTING TOPOGRAPHIC CONTOURS (2' INTERVALS)
	EXISTING PAVED ROAD
	EXISTING UNPAVED ROAD
	EXISTING RAILROAD
	WETLANDS
	CREEK/STREAM CENTERLINE
	LIMITS OF RIPARIAN PROTECTION AREA (PER FLUVANNA COUNTY ORDINANCE)
	APPROXIMATE EDGE OF SURFACE WATER
	LIMITS OF 100-YR FLOOD PLAIN
	BASE FLOOD ELEVATION (100-YEAR, SEE NOTE 4)
	EXISTING TREE LINE
	EXISTING FENCE
	EXISTING OVERHEAD UTILITY LINE
	EXISTING MONITORING WELL LOCATION AND IDENTIFICATION (CCR RULE)
	EXISTING OBSERVATION WELL LOCATION AND IDENTIFICATION
	EXISTING MANHOLE
	EXISTING SURFACE WATER FLOW DIRECTION

- ### GENERAL NOTES
- EXISTING CONDITIONS COMPILED FROM:
 - AERIAL TOPOGRAPHIC SURVEY PREPARED BY MCKENZIE SNYDER, INC., DATE OF AERIAL PHOTO: 1/16/15 [CONTROL PREPARED BY H&B SURVEYING & MAPPING (H&B)]
 - BOUNDARY SURVEY PREPARED BY H&B SURVEYING AND MAPPING, LLC DATED 04/27/15.
 - EXISTING TOPOGRAPHY WITHIN THE LIMITS OF THE WEST ASH POND BASED ON FIELD SURVEY BY H&B SURVEYING AND MAPPING DATED 07/06/17. TOPO REPRESENTS THE BOTTOM OF POND.
 - SITE DATUM: NAD83 / NAVD88
 - WETLAND DELINEATION BY DOMINION ENVIRONMENTAL SERVICES ON 01/30/15 & 02/05/15 AND BY GOLDER ASSOCIATES ON 03/16/15 & 03/25/15. WATERS OF THE U.S. CONFIRMED BY THE USACE DURING JUNE 4, 2015 SITE VISIT.
 - 100 YEAR FLOOD PLAIN DELINEATION BASED ON FLOOD ELEVATION DATA REPRESENTED ON FEMA FLOOD INSURANCE RATE MAP (FIRM), MAP NUMBER 51065C0260C, EFFECTIVE DATE: 05/16/2008.
 - THE MAJORITY OF WATER AND ASH HAS BEEN REMOVED FROM THE WEST ASH POND, AND ONLY MANAGED CONTACT STORMWATER IS PRESENT.



CLIENT
DOMINION ENERGY
BREMO POWER STATION
FLUVANNA COUNTY, VIRGINIA

CONSULTANT
GOLDER ASSOCIATES INC.
2108 WEST LABURNUM AVENUE
SUITE 200
RICHMOND, VA 23227
(804) 358-7900
www.golder.com

GOLDER

PROJECT
CLOSURE BY REMOVAL PLAN
WEST ASH POND & EAST ASH POND
SOLID WASTE PERMIT NO. 618

TITLE
WEST ASH POND
PRE-CLOSURE TOPOGRAPHY
(APPROXIMATE BOTTOM OF POND)

PROJECT NO.
15-20347

REV. 1
2 of 9
DRAWING
CBR-2

1" IF THIS MEASUREMENT DOES NOT MATCH WHAT IS SHOWN, THE SHEET SIZE HAS BEEN ADJUSTED FROM: ARCH D



	DOMINION PROPERTY BOUNDARY
	ADJACENT PROPERTY BOUNDARY
	CCR UNIT BOUNDARY
	EXISTING TOPOGRAPHIC CONTOURS (2' INTERVALS)
	EXISTING PAVED ROAD
	EXISTING UNPAVED ROAD
	EXISTING RAILROAD
	WETLANDS
	CREEK/STREAM CENTERLINE
	LIMITS OF RIPARIAN PROTECTION AREA (PER FLUVANNA COUNTY ORDINANCE)
	APPROXIMATE EDGE OF SURFACE WATER
	LIMITS OF 100-YR FLOOD PLAIN
	BASE FLOOD ELEVATION (100-YEAR, SEE NOTE 4)
	EXISTING TREE LINE
	EXISTING FENCE
	EXISTING OVERHEAD UTILITY LINE
	EXISTING MONITORING WELL LOCATION AND IDENTIFICATION (CCR RULE)
	EXISTING OBSERVATION WELL LOCATION AND IDENTIFICATION
	EXISTING MANHOLE
	EXISTING SURFACE WATER FLOW DIRECTION
	APPROXIMATE CLEAN CLOSURE PHASE LIMITS (SUBJECT TO CHANGE BASED ON FIELD CONDITIONS DURING EXCAVATION AND MAY INCLUDE SUB-PHASES)
	DENOTES APPROXIMATE LIMITS OF CRITICAL AREAS SUBJECT TO BACKFILL FOR ACCESS AND SLOPE STABILITY

1. EXISTING CONDITIONS COMPILED FROM:
 - a. AERIAL TOPOGRAPHIC SURVEY PREPARED BY MCKENZIE SNYDER, INC., DATE OF AERIAL PHOTO: 1/16/15 [CONTROL PREPARED BY H&B SURVEYING & MAPPING (H&B)]
 - b. BOUNDARY SURVEY PREPARED BY H&B SURVEYING AND MAPPING LLC DATED 04/27/15.
 - c. EXISTING TOPOGRAPHY WITHIN THE LIMITS OF THE WEST ASH POND BASED ON FIELD SURVEY BY H&B SURVEYING AND MAPPING DATED 07/06/17. TOPO REPRESENTS THE BOTTOM OF POND.
2. SITE DATUM: NAD83 / NAVD88
3. WETLAND DELINEATION BY DOMINION ENVIRONMENTAL SERVICES ON 01/30/15 & 02/05/15 AND BY GOLDBER ASSOCIATES ON 03/16/15 & 03/25/15. WATERS OF THE U.S. CONFIRMED BY THE USACE DURING JUNE 4, 2015 SITE VISIT.
4. 100 YEAR FLOOD PLAIN DELINEATION BASED ON FLOOD ELEVATION DATA REPRESENTED ON FEMA FLOOD INSURANCE RATE MAP (FIRM), MAP NUMBER 51065C0260C, EFFECTIVE DATE: 05/16/2008.

1. TOPOGRAPHY SHOWN WITHIN LIMITS OF THE WEST ASH POND, REPRESENTS THE POND BOTTOM BASED ON FIELD SURVEY BY H&B SURVEYING AND MAPPING DATED 07/06/17.
2. PHASED CLOSURE OF THE WEST POND MAY BE SEQUENCED AS NECESSARY TO ADDRESS ISSUES RELATED TO ACCESS AND SLOPE STABILITY, AND TO MINIMIZE CONTACT STORMWATER AREAS. SUB-PHASES MAY BE REQUIRED FOR REGULATORY APPROVAL.
3. ANY AREA CERTIFIED AS ACHIEVING CLOSURE BY REMOVAL IS TO BE PROTECTED FROM CCR AND CONTACT STORMWATER, AND MAY BE FILLED AND/OR RESHAPED AS NEEDED PRIOR TO ACHIEVING FINAL GRADES.
4. ACCUMULATED CCR SHALL BE REMOVED FROM SURFACES WITHIN THE POND LIMITS SUCH THAT NO CCR REMAINS VISIBLE.
5. FOLLOWING VISUAL-CLEAN CONDITIONS, OVER-EXCAVATE THE REMOVAL FOOTPRINT BY AT LEAST SIX INCHES.
6. VISUAL INSPECTION AND TARGETED SUBGRADE VISUAL SAMPLING TO BE OVERSEEN BY OWNER'S ENGINEER REPRESENTATIVE. SAMPLING TO BE PERFORMED AT A FREQUENCY OF AT LEAST ONE TEST PER ACRE. TARGETED SAMPLING TO CONSIST OF HAND-DUG HOLES AT LEAST SIX INCHES DEEP.
7. EXCAVATION OF SLOPES STEEPER THAN 2:1 SHALL BE SEQUENCED SUCH THAT THE SLOPES CAN BE EXCAVATED, INSPECTED, AND BACKFILLED IN THE SHORTEST TIME POSSIBLE. BACKFILL SLOPES WITH CLEAN SOIL FILL AT NO STEEPER THAN 2:1.
8. EXCAVATED CCR AND SOIL-CCR MIXTURES SHALL BE CONSOLIDATED IN NORTH ASH POND OR TAKEN TO AN OFF-SITE DISPOSAL FACILITY AS DIRECTED BY DOMINION.

REV.	MM/DD/YY	DESCRIPTION	DESIGN	CADD	CHECK	REVIEW
0	05/07/18	ISSUED FOR PERMIT	JRD	BPG	DPM	JRD
1	09/14/18	RESPONSE TO DEQ TR COMMENTS	JRD	BPG	DPM	JRD



CLIENT
DOMINION ENERGY
BREMEN POWER STATION
FLUVANNA COUNTY, VIRGINIA


GOLDER ASSOCIATES INC.
212108 WEST LABURNUM AVENUE
SUITE 200
RICHMOND, VA 23227
(804) 358-7900
www.golder.com



WEST ASH POND CLOSURE BY REMOVAL PLAN

PROJECT NO.
15-20347

Path: G:\Plan Production Data Files\Drawing Data Files\15-20347\DWG - EAP and WAP Closure by Removal\Active Drawings\1520347DCA_W0405.dwg

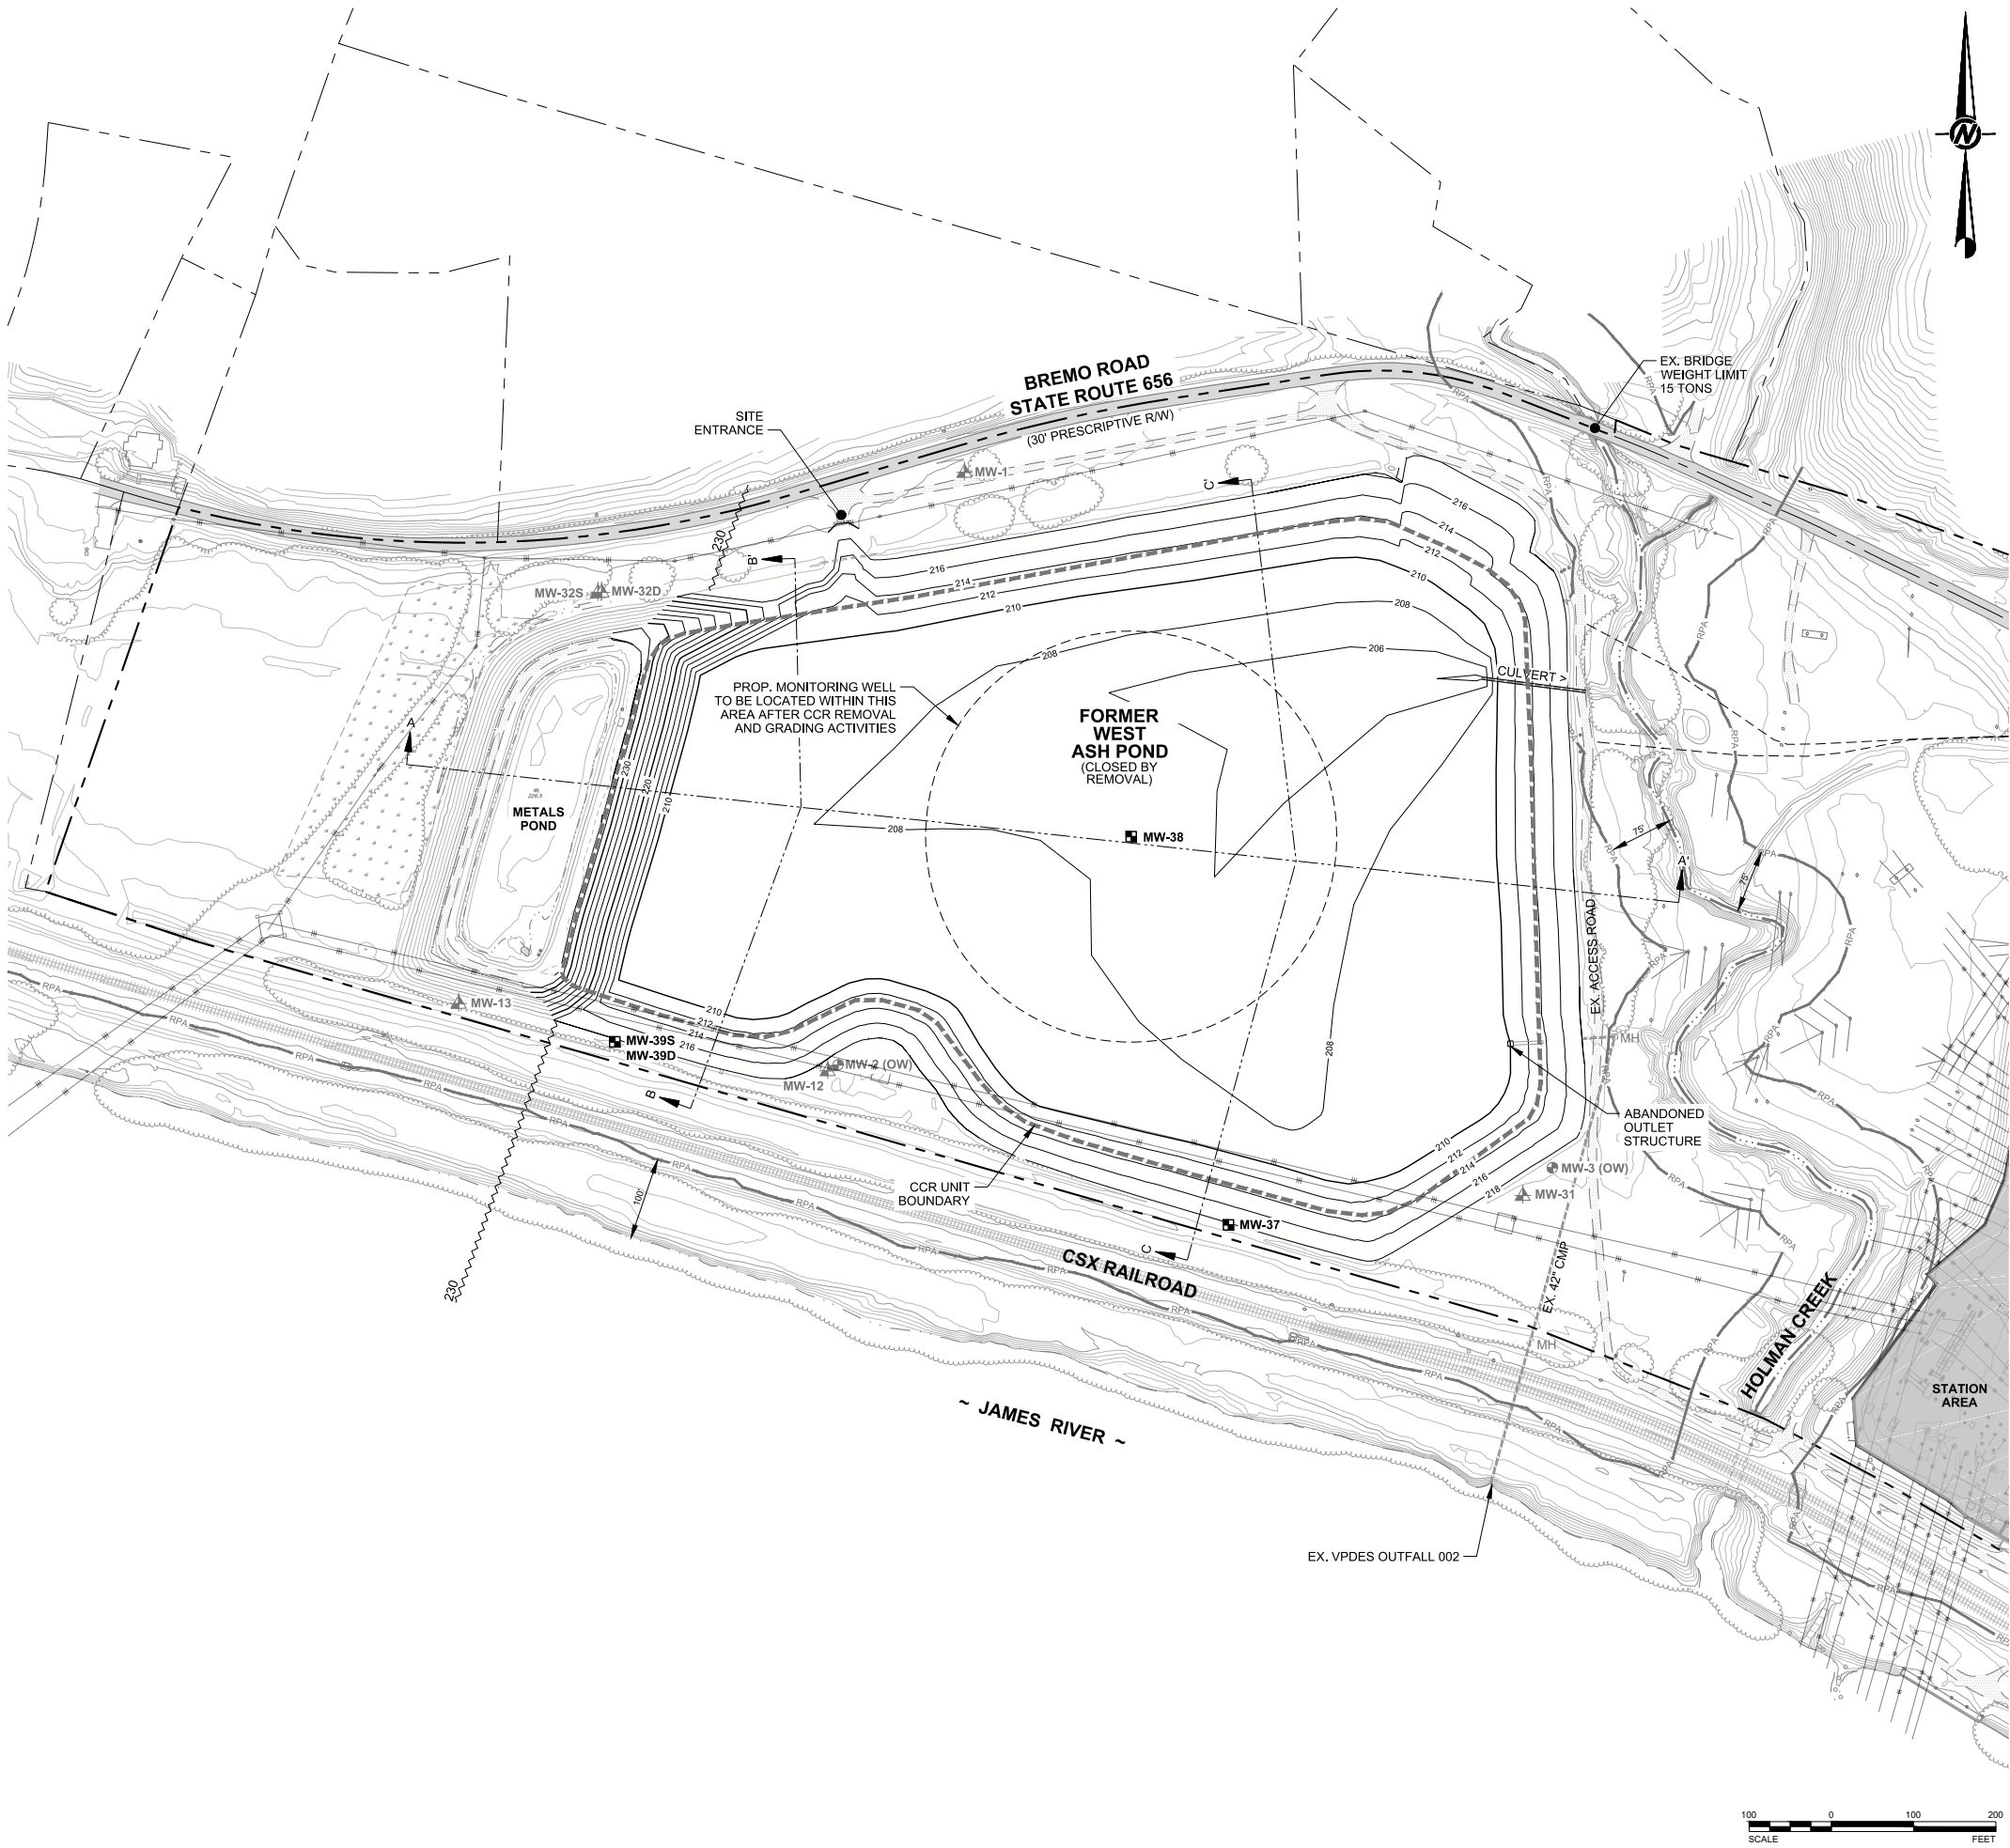

LEGEND	
	DOMINION PROPERTY BOUNDARY
	ADJACENT PROPERTY BOUNDARY
	CCR UNIT BOUNDARY
	EXISTING TOPOGRAPHIC CONTOURS (2' INTERVALS) (FROM AERIAL SURVEY - SEE GENERAL NOTE 1a)
	CONCEPTUAL FINAL GRADE CONTOURS (2' INTERVALS)
	EXISTING PAVED ROAD
	EXISTING UNPAVED ROAD
	EXISTING RAILROAD
	WETLANDS
	CREEK/STREAM CENTERLINE
	LIMITS OF RIPARIAN PROTECTION AREA (PER FLUVANNA COUNTY ORDINANCE)
	APPROXIMATE EDGE OF SURFACE WATER
	BASE FLOOD ELEVATION (100-YEAR, SEE NOTE 4)
	EXISTING TREE LINE
	EXISTING FENCE
	EXISTING OVERHEAD UTILITY LINE
	EXISTING MONITORING WELL LOCATION AND IDENTIFICATION (CCR RULE)
	EXISTING OBSERVATION WELL LOCATION AND IDENTIFICATION
	PROPOSED MONITORING WELL LOCATION AND IDENTIFICATION
	EXISTING MANHOLE

- GENERAL NOTES**
- EXISTING CONDITIONS COMPILED FROM:
 - AERIAL TOPOGRAPHIC SURVEY PREPARED BY MCKENZIE SNYDER, INC., DATE OF AERIAL PHOTO: 1/16/15 [CONTROL PREPARED BY H&B SURVEYING & MAPPING (H&B)]
 - BOUNDARY SURVEY PREPARED BY H&B SURVEYING AND MAPPING, LLC DATED 04/27/15.
 - SITE DATUM: NAD83 / NAVD88
 - WETLAND DELINEATION BY DOMINION ENVIRONMENTAL SERVICES ON 01/30/15 & 02/05/15 AND BY GOLDER ASSOCIATES ON 03/16/15 & 03/25/15. WATERS OF THE U.S. CONFIRMED BY THE USACE DURING JUNE 4, 2015 SITE VISIT.
 - 100 YEAR FLOOD PLAIN DELINEATION BASED ON FLOOD ELEVATION DATA REPRESENTED ON FEMA FLOOD INSURANCE RATE MAP (FIRM), MAP NUMBER 51065C0260C, EFFECTIVE DATE: 05/16/2008.

- CONCEPTUAL FINAL GRADING NOTE**
- CONCEPTUAL FINAL GRADING IS SHOWN FOR REFERENCE ONLY AND IS SUBJECT TO CHANGE.

PROJECT
CLOSURE BY REMOVAL PLAN
WEST ASH POND & EAST ASH POND
SOLID WASTE PERMIT NO. 618

TITLE
WEST ASH POND
CONCEPTUAL FINAL GRADING PLAN

PROJECT NO.
15-20347

CLIENT
DOMINION ENERGY
BREMO POWER STATION
FLUVANNA COUNTY, VIRGINIA

CONSULTANT
GOLDER ASSOCIATES INC.
2108 WEST LABURNUM AVENUE
SUITE 200
RICHMOND, VA 23227
(804) 358-7900
www.golder.com

GOLDER ASSOCIATES INC.
2108 WEST LABURNUM AVENUE
SUITE 200
RICHMOND, VA 23227
(804) 358-7900
www.golder.com

REV. 1

4 of 9

DRAWING
CBR-4

1

09/14/18

RESPONSE TO DEQ TR COMMENTS

JRD

DPM

JRD

0

05/07/18

ISSUED FOR PERMIT

JRD

BPG

JRD

REV.

MMDDYY

DESCRIPTION

DESIGN


CADD

CHECK


REVIEW

1" IF THIS MEASUREMENT DOES NOT MATCH WHAT IS SHOWN, THE SHEET SIZE HAS BEEN ADJUSTED FROM: ARCH D


Path: G:\Bin Production Data Filed\Drawing Data Filed\15-20347\DWG - EAP and WAP Closure by Removal\Active Drawings\1520347D0A_H04.05.dwg

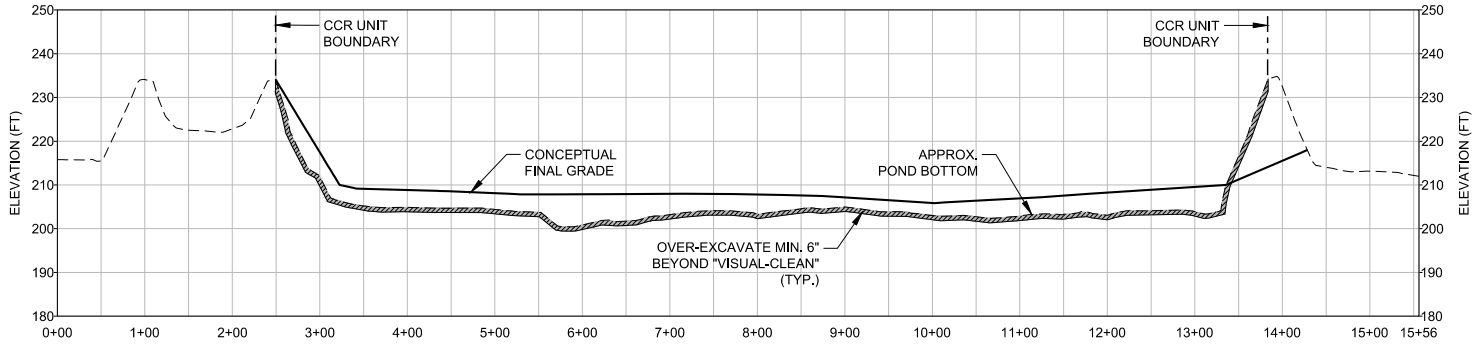

SECTION A - A'

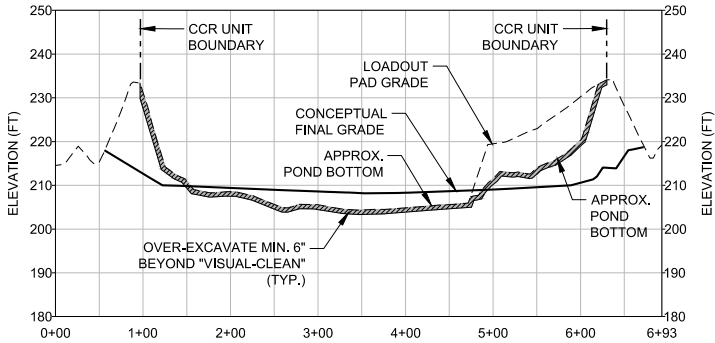

SECTION B - B'

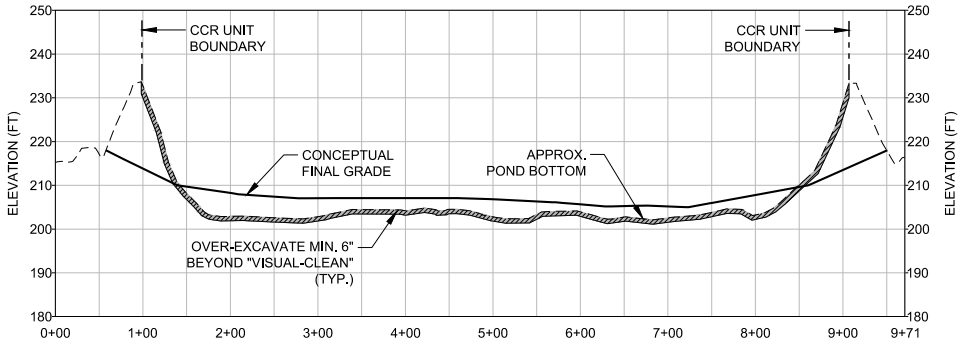

SECTION C - C'



PROJECT
CLOSURE BY REMOVAL PLAN
WEST ASH POND & EAST ASH POND
SOLID WASTE PERMIT NO. 618

TITLE
WEST ASH POND
CROSS-SECTIONS

PROJECT NO.
15-20347

CLIENT
DOMINION ENERGY
BREMO POWER STATION
FLUVANNA COUNTY, VIRGINIA

CONSULTANT




GOLDER ASSOCIATES INC.
2108 WEST LABURNUM AVENUE
SUITE 200
RICHMOND, VA 23227
(804) 358-7900
www.golder.com

SEAL




REV.	MMDDYY	DESCRIPTION	DESIGN	CADD	CHECK	REVIEW
1	09/14/18	RESPONSE TO DEQ TR COMMENTS	JRD	BPG	DPM	JRD
0	05/07/18	ISSUED FOR PERMIT	JRD	BPG	DPM	JRD

1" IF THIS MEASUREMENT DOES NOT MATCH WHAT IS SHOWN, THE SHEET SIZE HAS BEEN ADJUSTED FROM ARCH D

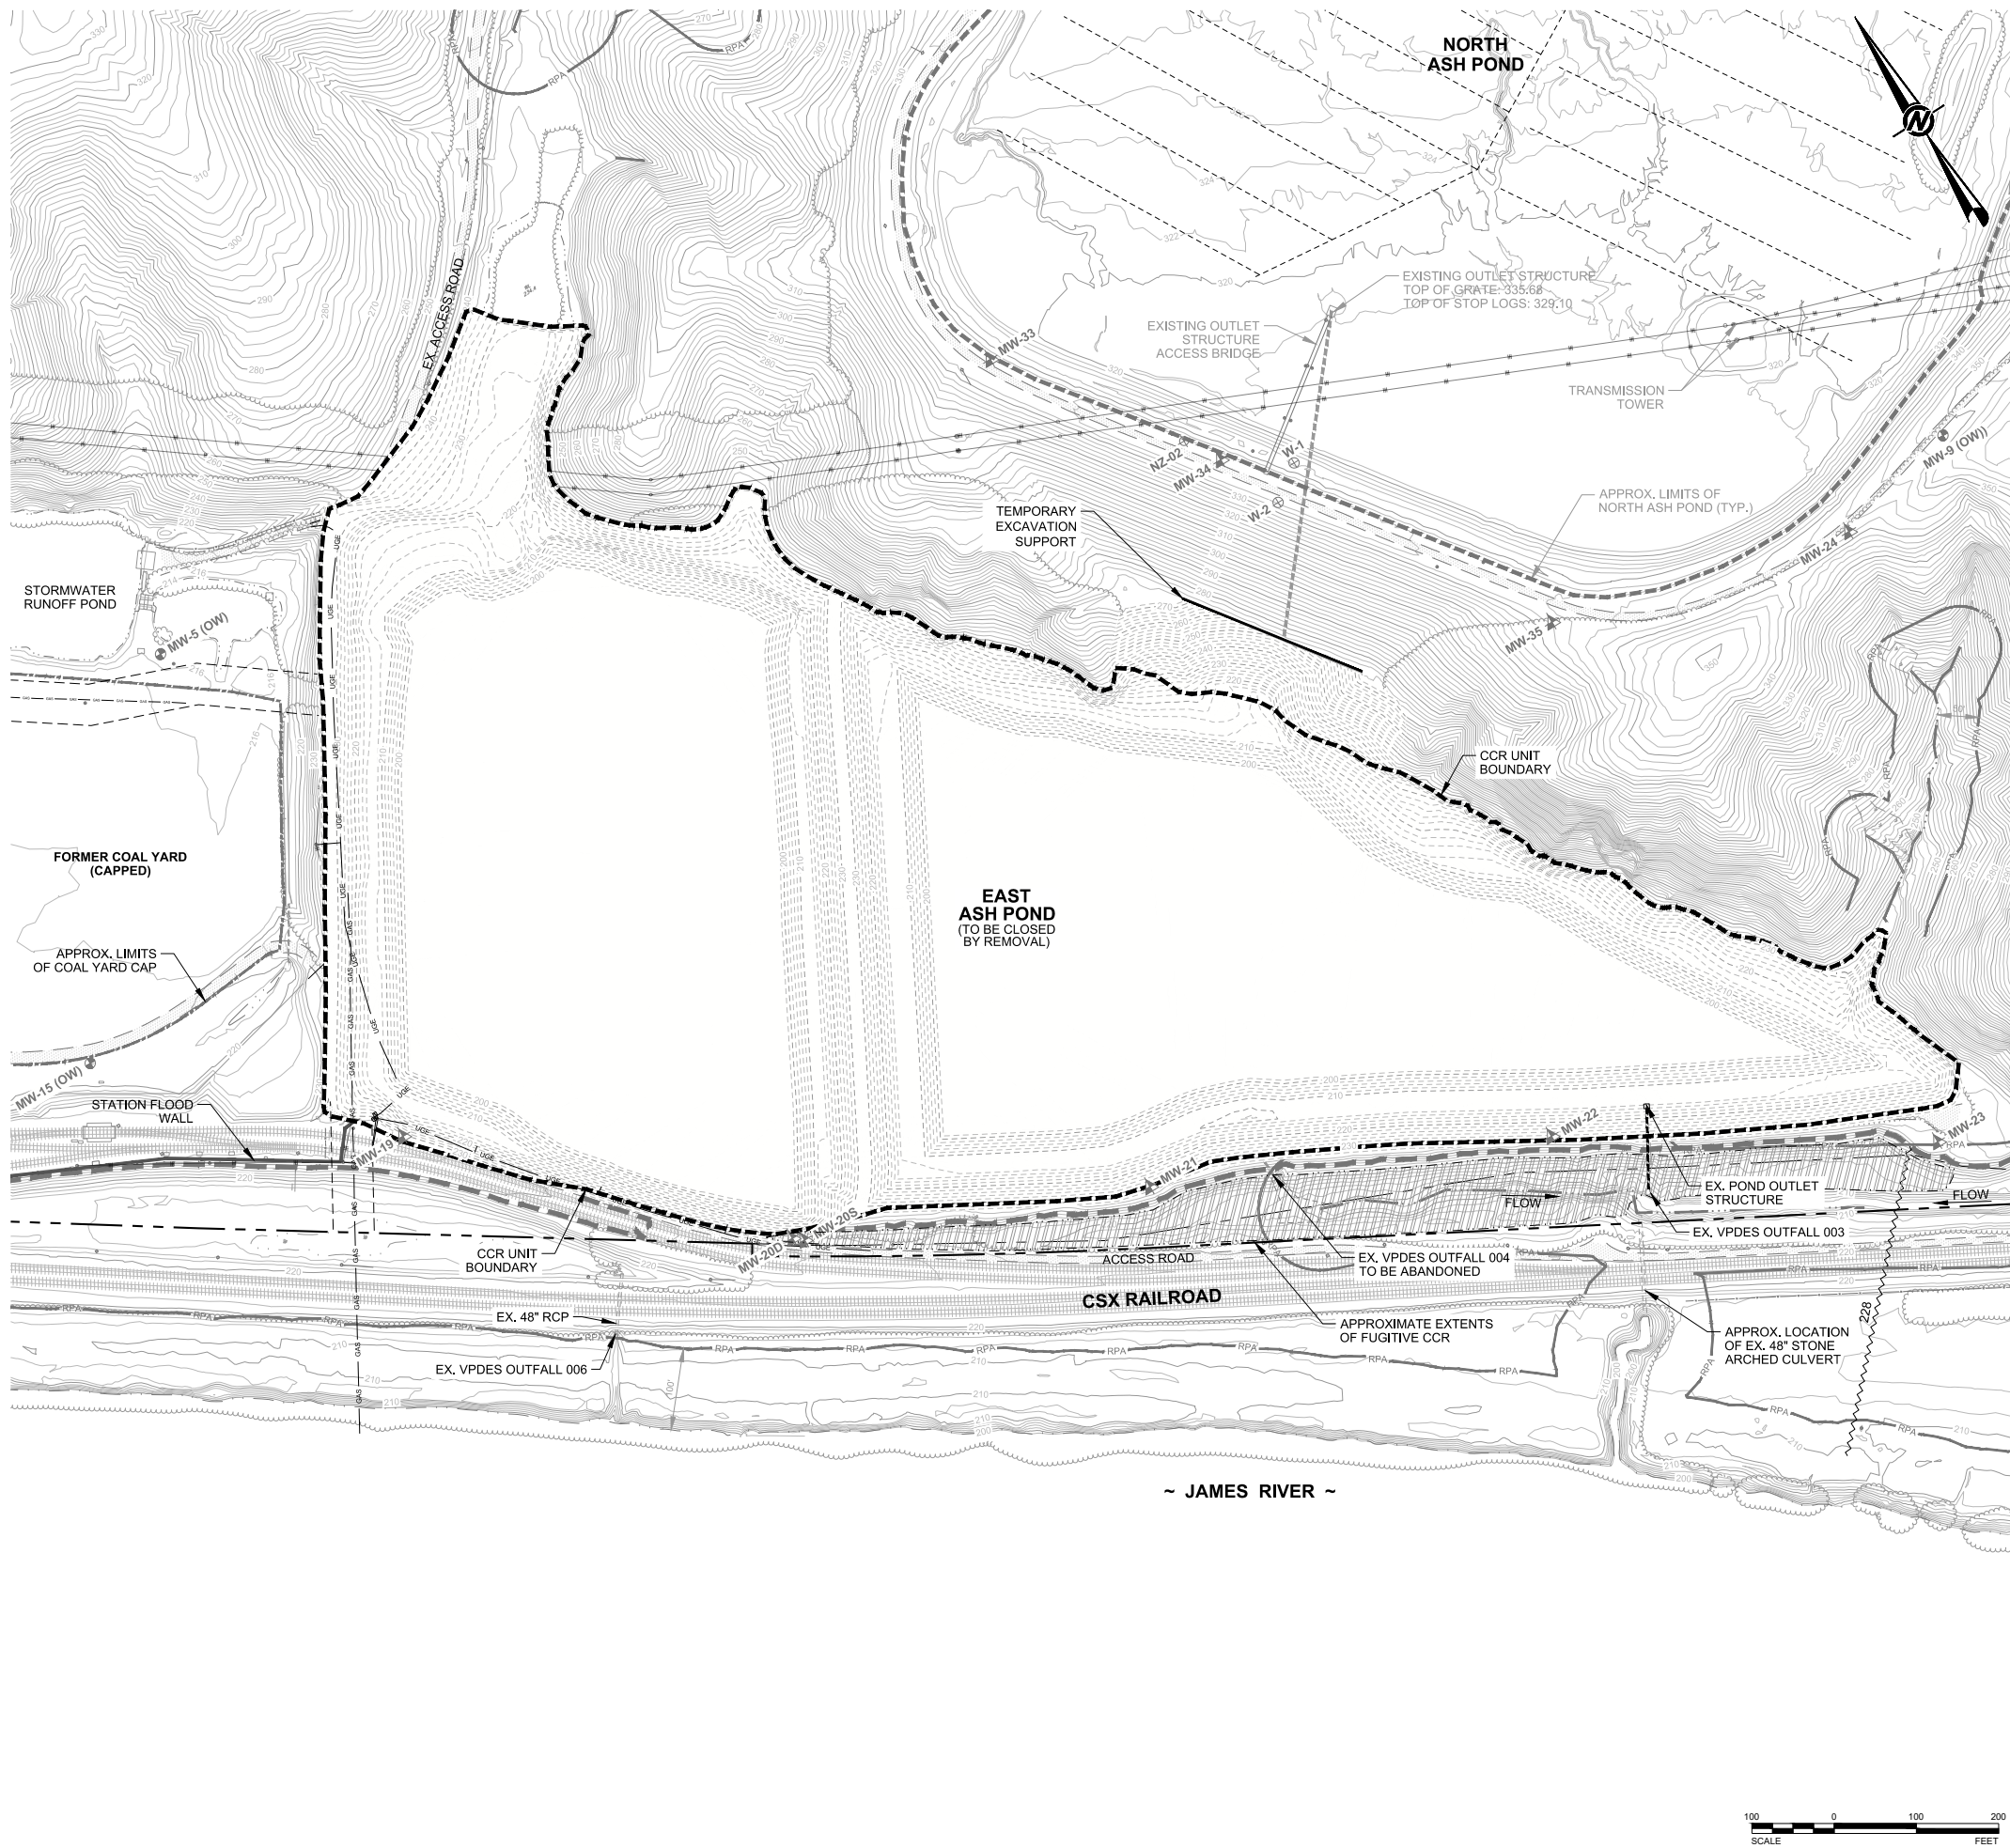

IF THIS MEASUREMENT DOES NOT MATCH WHAT IS SHOWN, THE SHEET SIZE HAS BEEN MODIFIED FROM: ARCH D

Path: G:\Pics Production Data Files\15-20347\0411 - EAP and WAP Closure by Removal\Active Drawings\1520347\04A_M06-07.dwg

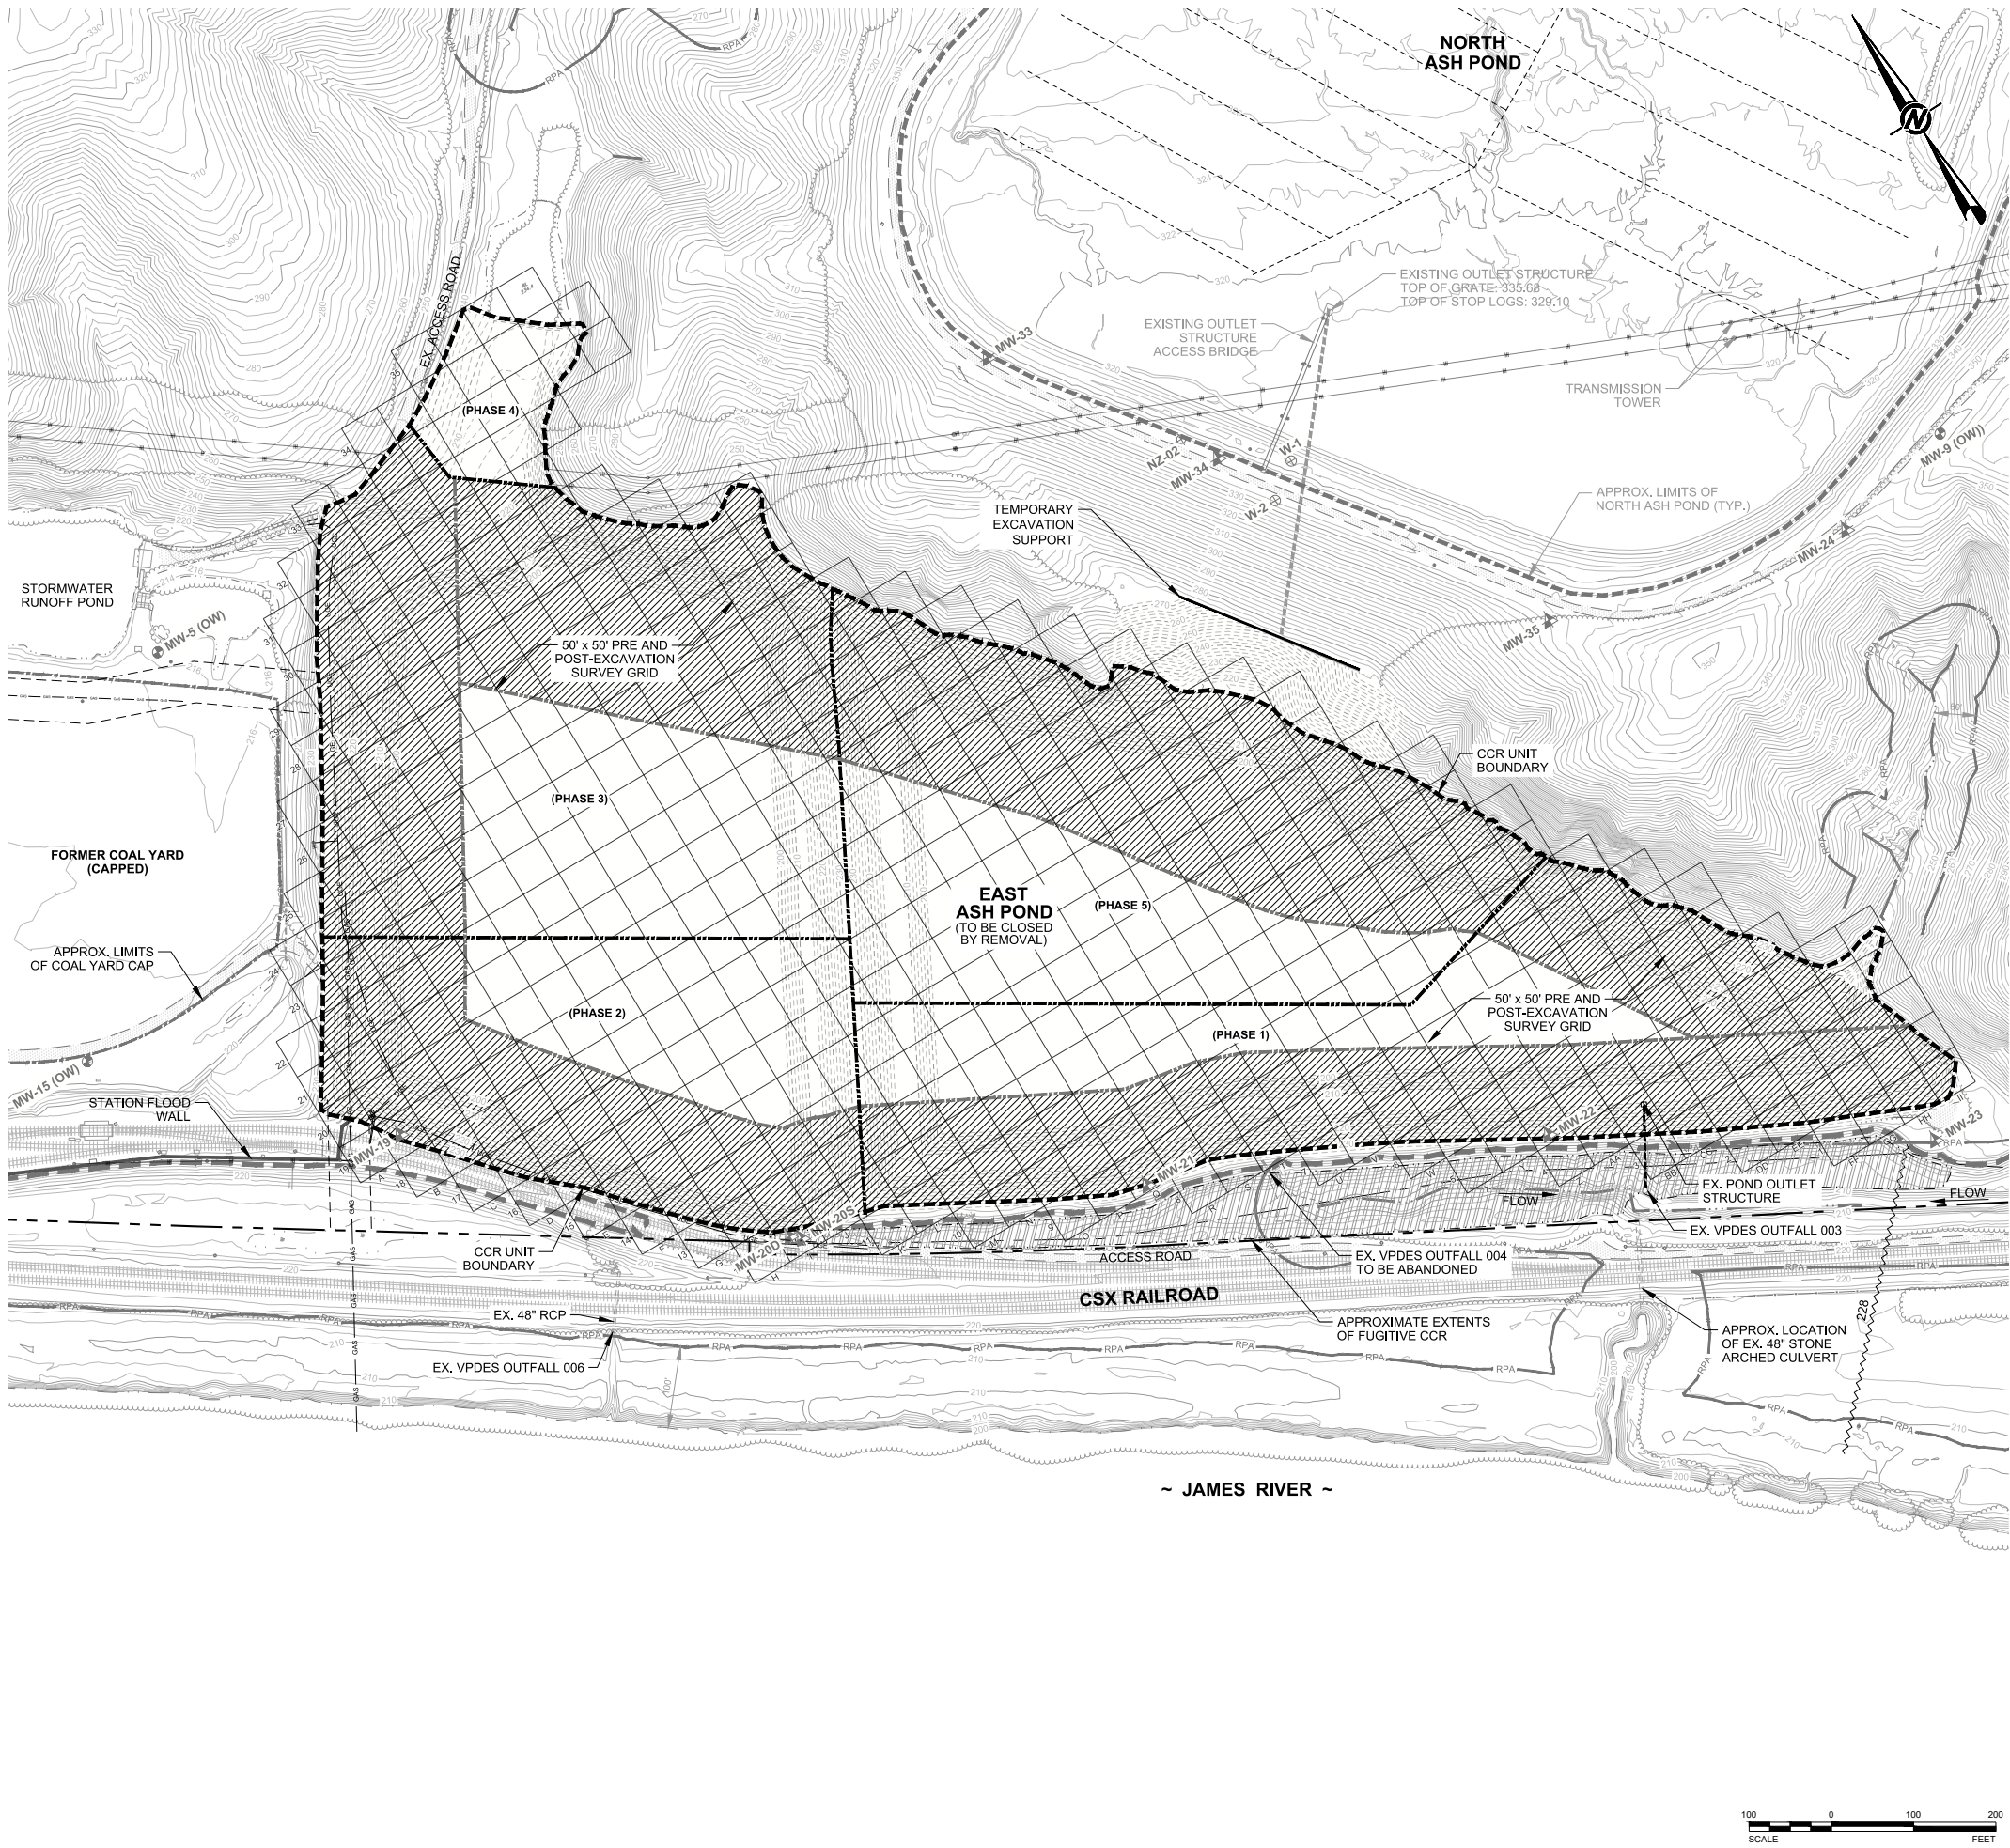

LEGEND

	DOMINION PROPERTY BOUNDARY
	ADJACENT PROPERTY BOUNDARY
	CCR UNIT BOUNDARY
	EXISTING TOPOGRAPHIC CONTOURS (2' INTERVALS) (FROM AERIAL SURVEY - SEE GENERAL NOTE 1a)
	APPROX. POND BOTTOM CONTOURS (2' INTERVALS) (SEE GENERAL NOTE 1c)
	EXISTING UNPAVED ROAD
	EXISTING RAILROAD
	WETLANDS
	CREEK/STREAM CENTERLINE
	LIMITS OF RIPARIAN PROTECTION AREA (PER FLUVANNA COUNTY ORDINANCE)
	APPROXIMATE EDGE OF SURFACE WATER
	LIMITS OF 100-YR FLOOD PLAIN
	BASE FLOOD ELEVATION (100-YEAR, SEE NOTE 4)
	EXISTING TREE LINE
	EXISTING FENCE
	EXISTING OVERHEAD UTILITY LINE
	EXISTING UNDERGROUND ELECTRIC LINE
	EXISTING UNDERGROUND GAS LINE
	EXISTING MONITORING WELL LOCATION AND IDENTIFICATION (CCR RULE)
	EXISTING OBSERVATION WELL LOCATION AND IDENTIFICATION
	EXISTING PIEZOMETER AND IDENTIFICATION
	EXISTING MANHOLE
	APPROXIMATE CLEAN CLOSURE PHASE LIMITS (SUBJECT TO CHANGE BASED ON FIELD CONDITIONS DURING EXCAVATION AND MAY INCLUDE SUB-PHASES)
	DENOTES APPROXIMATE LIMITS OF CRITICAL AREAS SUBJECT TO BACKFILL FOR ACCESS AND SLOPE STABILITY

GENERAL NOTES


- EXISTING CONDITIONS COMPILED FROM:
 - AERIAL TOPOGRAPHIC SURVEY PREPARED BY MCKENZIE SNYDER, INC., DATE OF AERIAL PHOTO: 1/16/15 [CONTROL PREPARED BY H&B SURVEYING & MAPPING (H&B)]
 - BOUNDARY SURVEY PREPARED BY H&B SURVEYING AND MAPPING, LLC DATED 04/27/15.
 - TOPOGRAPHY WITHIN THE LIMITS OF THE EAST ASH POND BASED ON THE APPROXIMATE POND BOTTOM PER HISTORICAL INFORMATION.
- SITE DATUM: NAD83 / NAVD88
- WETLAND DELINEATION BY DOMINION ENVIRONMENTAL SERVICES ON 01/30/15 & 02/05/15 AND BY GOLDER ASSOCIATES ON 03/16/15 & 03/25/15. WATERS OF THE U.S. CONFIRMED BY THE USACE DURING JUNE 4, 2015 SITE VISIT.
- 100 YEAR FLOOD PLAIN DELINEATION BASED ON FLOOD ELEVATION DATA REPRESENTED ON FEMA FLOOD INSURANCE RATE MAP (FIRM), MAP NUMBER 51065C0260C, EFFECTIVE DATE: 05/16/2008.

CLOSURE BY REMOVAL NOTES

- TOPOGRAPHY SHOWN WITHIN LIMITS OF THE EAST ASH POND REPRESENTS THE APPROXIMATE BOTTOM BASED ON HISTORIC DRAWINGS AND FIELD INFORMATION. FOR REFERENCE ONLY.
- PHASED CLOSURE OF EAST ASH POND MAY BE SEQUENCED AS NECESSARY TO SUPPORT CONSTRUCTION AND MAY INCLUDE SUB-PHASES FOR REGULATORY APPROVAL TO SUPPORT ACCESS, SLOPE STABILITY, AND MINIMIZE CONTACT STORMWATER AREAS.
- ANY AREA CERTIFIED AS ACHIEVING CLOSURE BY REMOVAL IS TO BE PROTECTED FROM CCR AND CONTACT STORMWATER, AND MAY BE FILLED AND/OR RESHAPED PRIOR TO ACHIEVING FINAL GRADES.
- ACCUMULATED CCR SHALL BE REMOVED FROM SURFACES WITHIN THE POND LIMITS SUCH THAT NO CCR REMAINS VISIBLE.
- FOLLOWING VISUAL-CLEAN CONDITIONS, OVER-EXCAVATE THE REMOVAL FOOTPRINT BY AT LEAST SIX INCHES.
- VISUAL INSPECTION AND TARGETED SUBGRADE VISUAL SAMPLING TO BE OVERSEEN BY OWNER'S ENGINEER REPRESENTATIVE. SAMPLING TO BE PERFORMED AT A FREQUENCY OF AT LEAST ONE TEST PER ACRE. TARGETED SAMPLING TO CONSIST OF HAND-DUG HOLES AT LEAST SIX INCHES DEEP.
- EXCAVATION OF SLOPES STEEPER THAN 2:1 SHALL BE SEQUENCED SUCH THAT THE SLOPES CAN BE EXCAVATED, INSPECTED, AND BACKFILLED IN THE SHORTEST TIME POSSIBLE. BACKFILL SLOPES WITH CLEAN SOIL FILL AT NO STEEPER THAN 2:1.
- EXCAVATED CCR AND SOIL-CCR MIXTURES SHALL BE CONSOLIDATED IN NORTH ASH POND OR TAKEN TO AN OFF-SITE DISPOSAL FACILITY AS DIRECTED BY DOMINION.

PROJECT	CLIENT				CONSULTANT			
	DOMINION ENERGY				GOLDER ASSOCIATES INC.			
	CLOSURE BY REMOVAL PLAN				2108 WEST LABURNUM AVENUE			
	WEST ASH POND & EAST ASH POND				SUITE 200			
TITLE	BREMO POWER STATION				RICHMOND, VA 23227			
	FLUVANNA COUNTY, VIRGINIA				(804) 358-7900			
	SOLID WASTE PERMIT NO. 618				www.golder.com			
	EAST ASH POND							
PROJECT NO.	CLOSURE BY REMOVAL PLAN							
	15-20347							
REV.	1	7	9	DRAWING	DRAWING			
				CBR-7				

Path: G:\Plan Production Data Files\Drawing Data Files\15-20347\DWG - EAP and WAP Closure by Removal\Active Drawings\1520347.DWG, W08.dwg

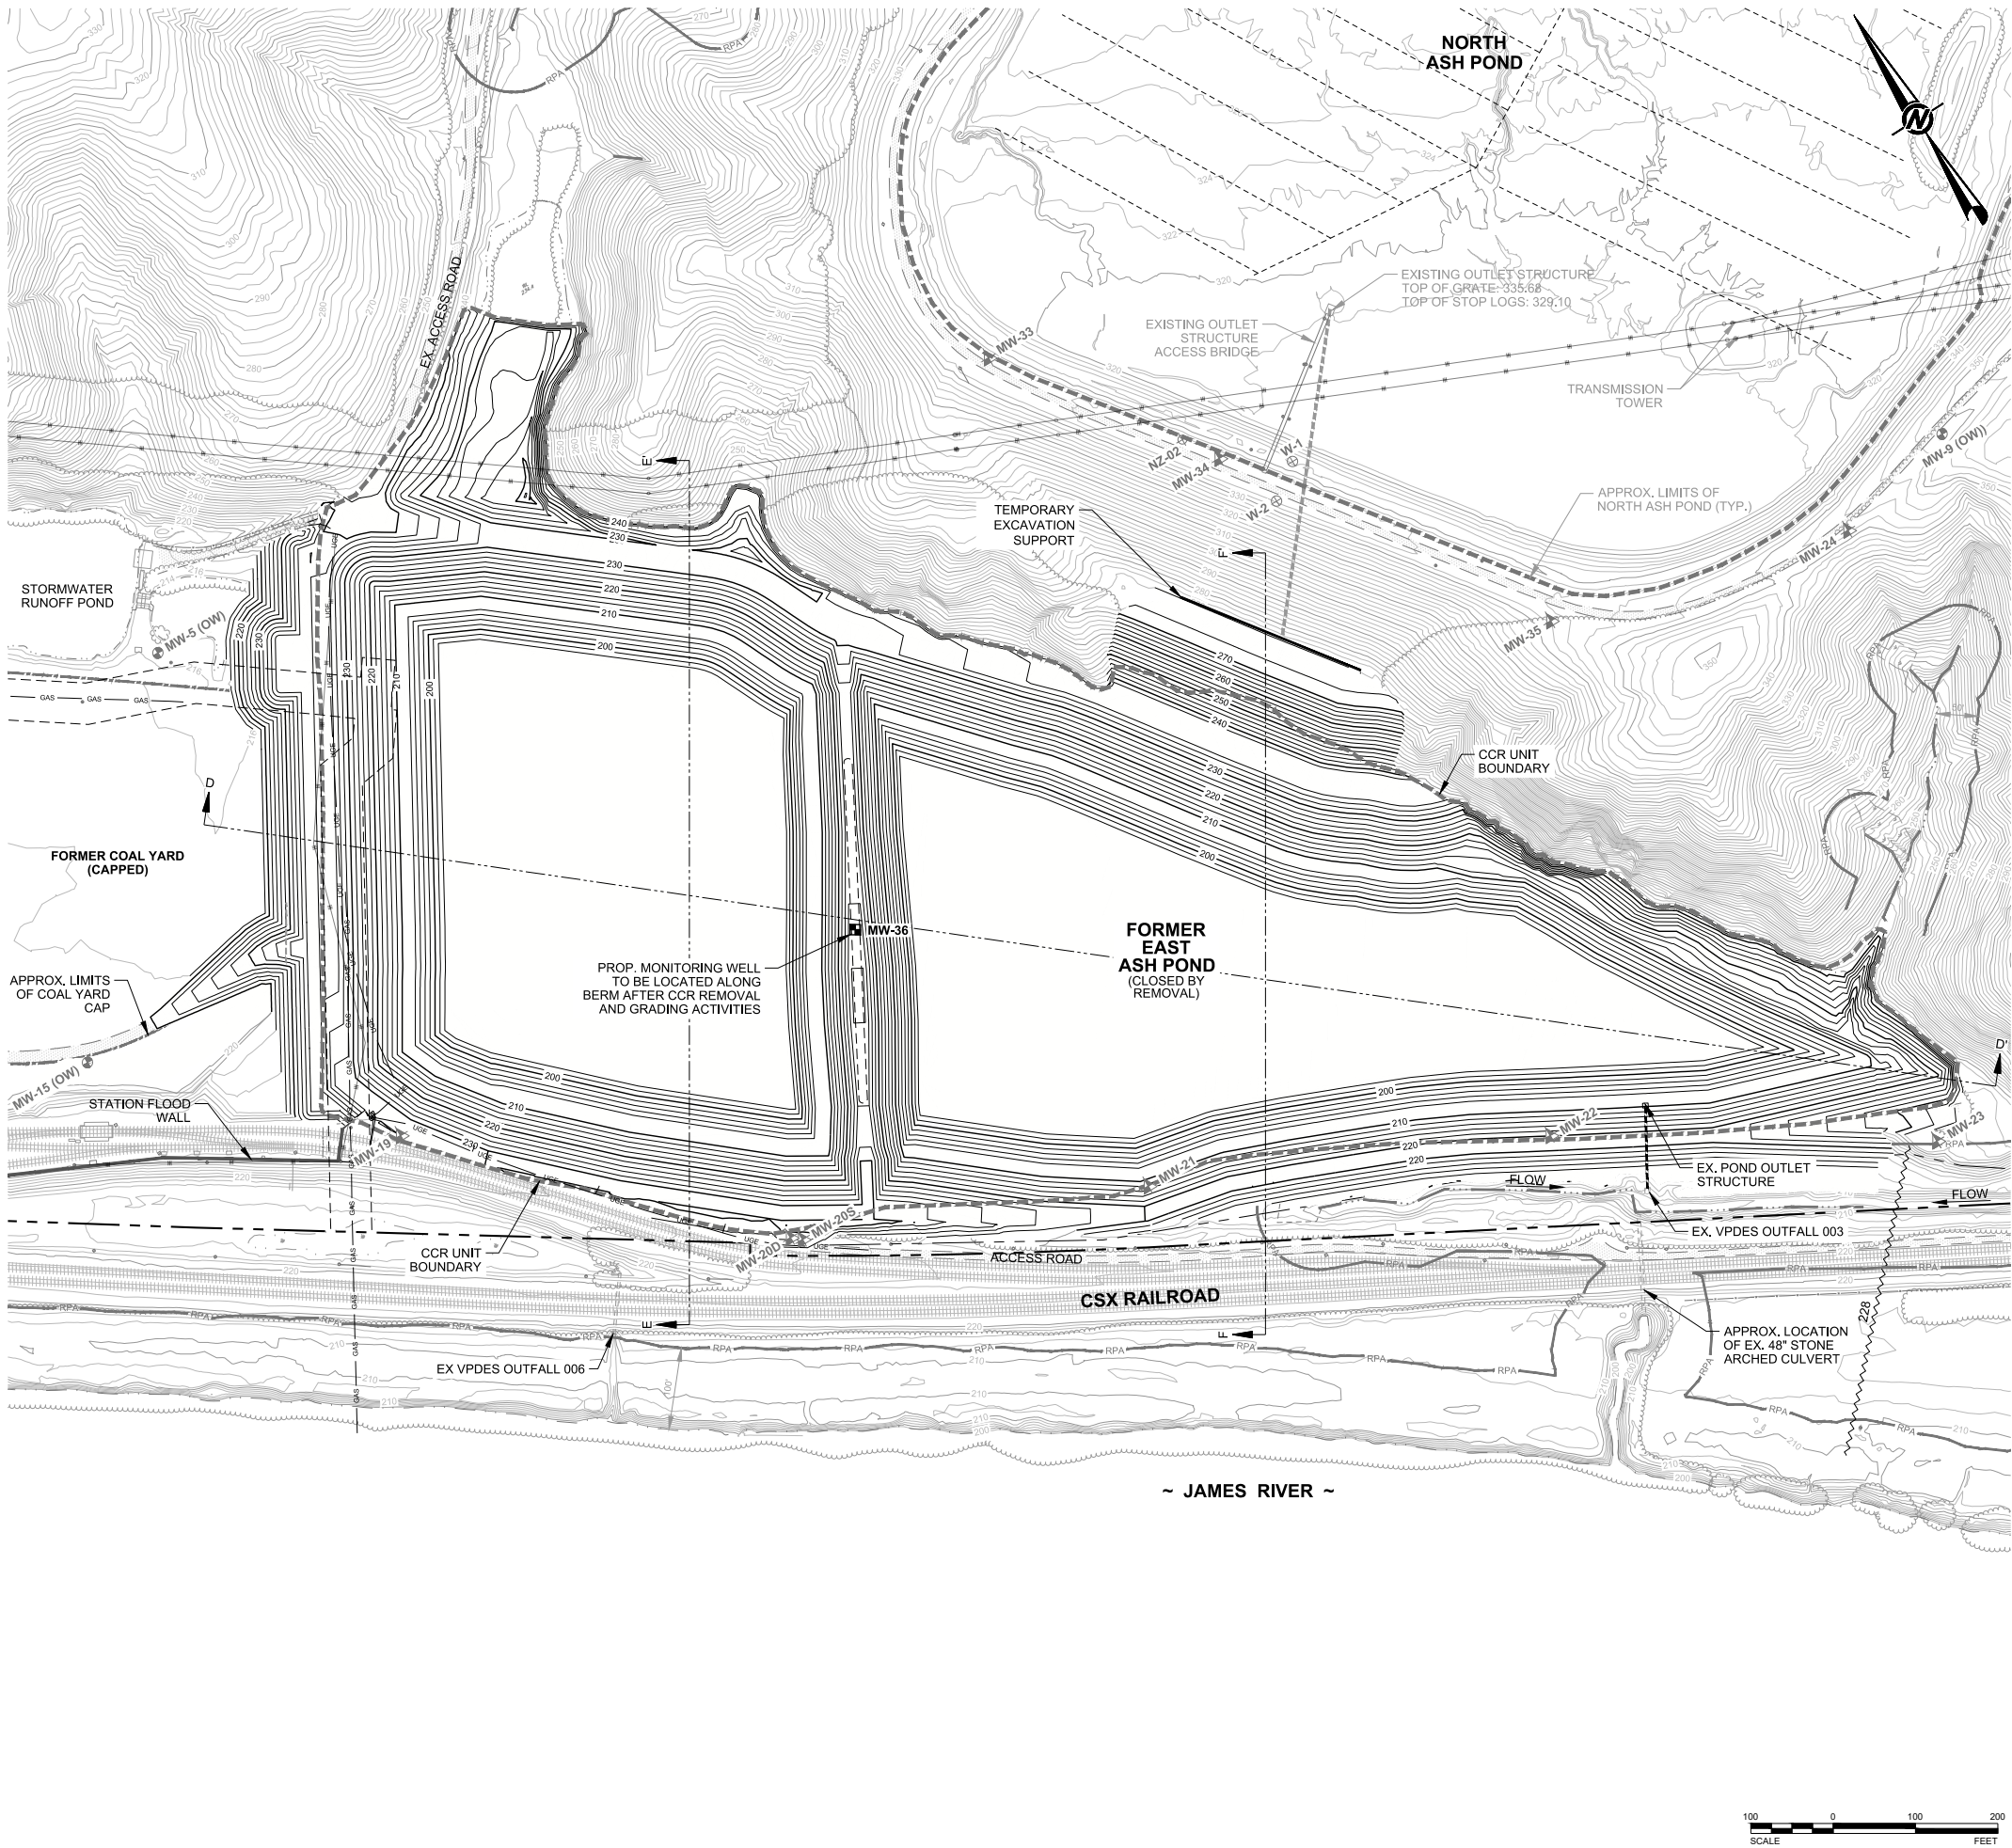

LEGEND

	DOMINION PROPERTY BOUNDARY
	ADJACENT PROPERTY BOUNDARY
	CCR UNIT BOUNDARY
	EXISTING TOPOGRAPHIC CONTOURS (2' INTERVALS) (FROM AERIAL SURVEY - SEE GENERAL NOTE 1a)
	CONCEPTUAL FINAL GRADE CONTOURS (2' INTERVALS)
	EXISTING UNPAVED ROAD
	EXISTING RAILROAD
	WETLANDS
	CREEK/STREAM CENTERLINE
	LIMITS OF RIPARIAN PROTECTION AREA (PER FLUVANNA COUNTY ORDINANCE)
	APPROXIMATE EDGE OF SURFACE WATER
	BASE FLOOD ELEVATION (100-YEAR, SEE NOTE 4)
	EXISTING TREE LINE
	EXISTING FENCE
	EXISTING OVERHEAD UTILITY LINE
	EXISTING UNDERGROUND ELECTRIC LINE
	EXISTING UNDERGROUND GAS LINE
	EXISTING MONITORING WELL LOCATION AND IDENTIFICATION (CCR RULE)
	EXISTING OBSERVATION WELL LOCATION AND IDENTIFICATION
	PROPOSED MONITORING WELL LOCATION AND IDENTIFICATION
	EXISTING PIEZOMETER AND IDENTIFICATION
	EXISTING MANHOLE

GENERAL NOTES

- EXISTING CONDITIONS COMPILED FROM:
 - AERIAL TOPOGRAPHIC SURVEY PREPARED BY MCKENZIE SNYDER, INC., DATE OF AERIAL PHOTO: 1/16/15 [CONTROL PREPARED BY H&B SURVEYING & MAPPING (H&B)]
 - BOUNDARY SURVEY PREPARED BY H&B SURVEYING AND MAPPING, LLC DATED 04/27/15.
- SITE DATUM: NAD83 / NAVD88
- WETLAND DELINEATION BY DOMINION ENVIRONMENTAL SERVICES ON 01/30/15 & 02/05/15 AND BY GOLDER ASSOCIATES ON 03/16/15 & 03/25/15. WATERS OF THE U.S. CONFIRMED BY THE USACE DURING JUNE 4, 2015 SITE VISIT.
- 100 YEAR FLOOD PLAIN DELINEATION BASED ON FLOOD ELEVATION DATA REPRESENTED ON FEMA FLOOD INSURANCE RATE MAP (FIRM), MAP NUMBER 51065C0260C, EFFECTIVE DATE: 05/16/2008.

CONCEPTUAL FINAL GRADING NOTE

- CONCEPTUAL FINAL GRADING IS SHOWN FOR REFERENCE ONLY AND IS SUBJECT TO CHANGE.

PROJECT
CLOSURE BY REMOVAL PLAN
WEST ASH POND & EAST ASH POND
SOLID WASTE PERMIT NO. 618

TITLE
EAST ASH POND
CONCEPTUAL FINAL GRADING PLAN

PROJECT NO.
15-20347

CLIENT
DOMINION ENERGY
BREMO POWER STATION
FLUVANNA COUNTY, VIRGINIA

CONSULTANT

GOLDER ASSOCIATES INC.
2108 WEST LABURNUM AVENUE
SUITE 200
RICHMOND, VA 23227
(804) 358-7900
www.golder.com




SEAL

REV. 1 8 OF 9


DRAWING
CCR-8

1" IF THIS MEASUREMENT DOES NOT MATCH WHAT IS SHOWN, THE SHEET SIZE HAS BEEN ADJUSTED FROM: ARCH D


Path: G:\Plan Production Data Files\Drawing Data Files\15-20347\DWG - E-AP and WAP Closure by Removal\Active Drawings\1520347D0A_V02.dwg

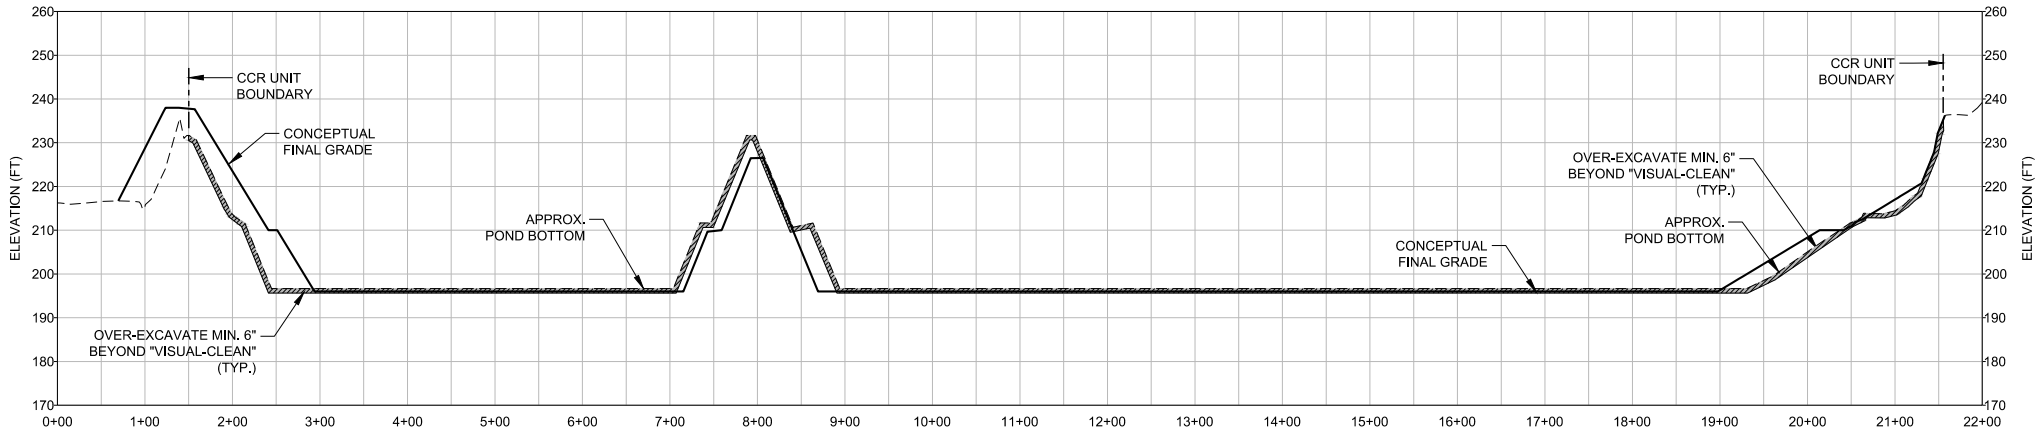

SECTION D - D'

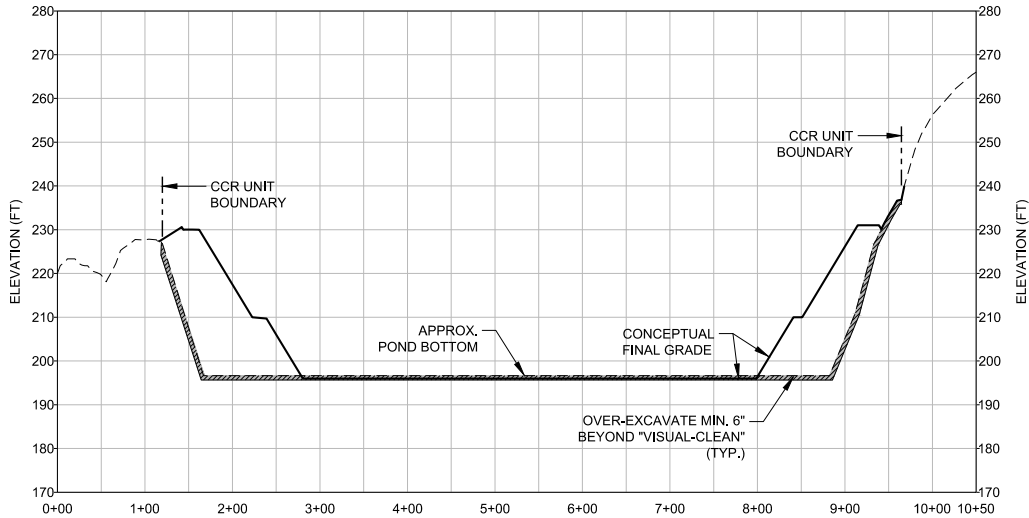

SECTION E - E'

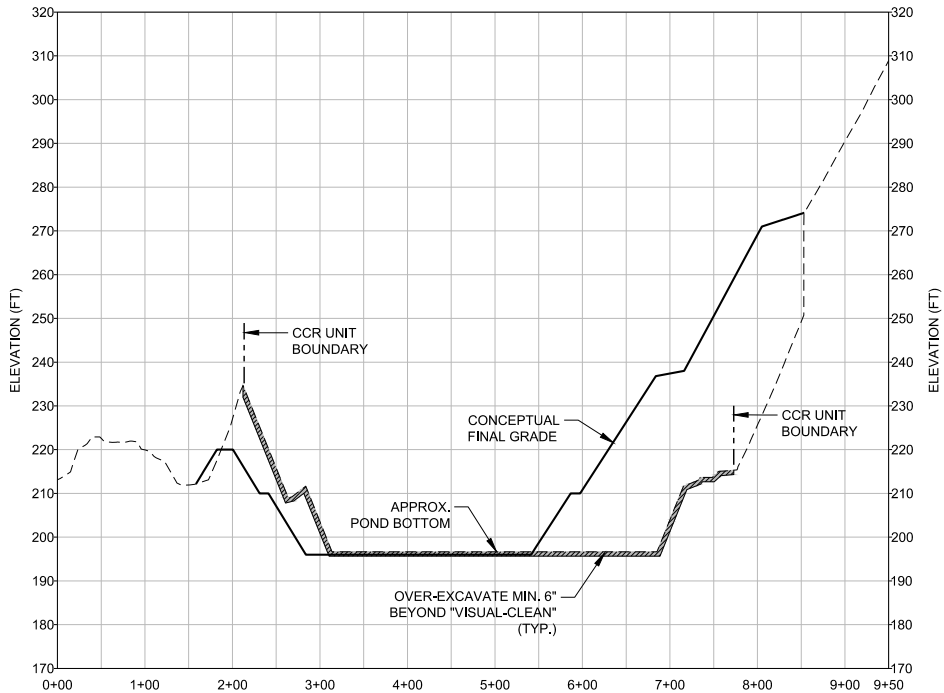

SECTION F - F'



PROJECT
CLOSURE BY REMOVAL PLAN
WEST ASH POND & EAST ASH POND
SOLID WASTE PERMIT No. 618

TITLE
EAST ASH POND
CROSS-SECTIONS

PROJECT NO.
15-20347

CLIENT
DOMINION ENERGY
BREMO POWER STATION
FLUVANNA COUNTY, VIRGINIA

CONSULTANT



GOLDER ASSOCIATES INC.
2108 WEST LABURNUM AVENUE
SUITE 200
RICHMOND, VA 23227
(804) 358-7900
www.golder.com


SEAL



REV.	MMDDYY	DESCRIPTION	DESIGN	CADD	CHECK	REVIEW
1	09/14/18	RESPONSE TO DEQ TR COMMENTS	JRD	BPG	DPM	JRD
0	05/07/18	ISSUED FOR PERMIT	JRD	BPG	DPM	JRD



Solid Waste Disposal Facility Cost Estimate Form

Facility Name:		Bremono Power Station CCR Impoundments				Permit No. SWP		618	
Address:		1038 Bremono Road							
City:	Bremono Bluff	State:	VA			Zip:	23022		
FA Holder:		Dominion Energy Virginia							
Estimate Prepared By:		Golder Associates Inc.							
Indicate the plan versions for which this cost estimate was prepared, identifying the following information for each plan:									
Closure Plan					Post-Closure Care Plan				
Title:	Surface Impoundment Closure Plan				Title:	n/a			
Plan Date:	May 2018	Approved:				Plan Date:		Approved:	
Consultant:	Golder Associates Inc.				Consultant:				
Corrective Action Plan					Corrective Action Monitoring Plan				
Title:	n/a				Title:	n/a			
Plan Date:		Approved:				Plan Date:		Approved:	
Consultant:					Consultant:				
Cost Estimate Summary									
Total Closure Cost:		\$18,041,661							
Total Post-Closure Cost:		\$0							
Total Corrective Action Cost:		\$0							
TOTAL:		\$18,041,661							
References									
Please indicate references used to develop this cost estimate: Unit costs were developed from 2016 closure construction bid estimates for Dominion's CCR impoundment facilities, estimates of soil prices in the coastal Virginia area, and other landfill closure bid packages in the consultant's local area.									
Certification by Preparer:									
This is to certify that the cost estimates pertaining to the engineering features and monitoring requirements of this solid waste management facility have been prepared by me and are representative of the design specified in the facility's approved Closure, Post-Closure and Corrective Action Plans. The estimate is based on the cost of hiring a third party and does not incorporate any salvage value that may be realized by the sale of wastes, facility structures, or equipment, land or other facility assets at the time of partial or final closure. In my professional judgment, the cost estimates are a true, correct, and complete representation of the financial liabilities for closure, post-closure care, and corrective action of the facility and comply with the requirements of 9 VAC 20-70 and all other DEQ rules and statutes of the Commonwealth of Virginia.									
Name:	Ron DiFrancesco, P.E.				Signature:				
Title:	Principal and Practice Leader				Date:	9-14-18			
Acknowledgement by Owner/Operator:									
Name:	David Craymer				Signature:				
Title:	Vice President, Power Generation Systems Operations				Date:	09/07/18			

Bremo Power Station - Permit #618
East Ash Pond CCR Impoundment Closure by Removal Cost Estimate

Item No.	Description	Unit of Measure	Quantity	Unit Price	Total	Notes/Assumptions
1	Demobilization	LS	1	\$ 1,099,687	\$ 1,099,687	
2	General Conditions	MO	6	\$ 203,688	\$ 1,222,128	
3	Construction Engineering / Surveying / Permitting	MO	6	\$ 20,000	\$ 120,000	Existing E&S Plan amendment
4	Maintain and inspect erosion / stormwater controls during	MO	6	\$ 8,000	\$ 48,000	
5	Dewatering	MO	6	\$ 553,369	\$ 3,320,214	
6	Stormwater Maintenance	MO	6	\$ 24,185	\$ 145,110	
7	Silt Fence non-reinforced	LF	3,500	\$ 4.27	\$ 14,945	
8	Silt Fence removal and disposal	LF	7,527	\$ 3.37	\$ 25,366	
9	CCR Excavation	CY	150,000	\$ 6.50	\$ 975,000	
10	6-inch over-excavation (26.5 acres)	CY	21,375	\$ 6.50	\$ 138,938	Excavate, load, haul and place in NAP
11	Soil backfill for slope stabilization	CY	250,000	\$ 25.00	\$ 6,250,000	Excavate, load, place and compact.
12	Site stabilization	Ac	27	\$ 3,500.00	\$ 94,500	
13	Closure sign	Ea	1	\$ 125	\$ 125	
14	Contingency	%	13,454,012	10%	\$ 1,345,401	
15	3rd party certification survey	Ac	27	\$ 4,500	\$ 119,250	
16	Construction QA/QC oversight	MO	6	\$ 20,000	\$ 120,000	
16	Closure certification report	LS	1	\$ 8,000	\$ 8,000	
17	Groundwater Monitoring	LS	1	\$ 66,380	\$ 66,380	Minimum remaining sampling events to demonstrate closure
	Total				\$ 15,113,044	

Notes: 1. Estimate based on starting with current condition as of September 14, 2018 to achieve clean closure condition

Bremo Power Station - Permit #618
West Ash Pond CCR Impoundment Closure by Removal Cost Estimate

Item No.	Description	Unit of Measure	Quantity	Unit Price	Total	Notes/Assumptions
1	Mobilization/Demobilization General Conditions	LS	1	\$ 75,000	\$ 75,000	
2	Construction Engineering / Surveying / Permitting	LS	1	\$ 35,000	\$ 35,000	Existing E&S Plan amendment
3	Maintain and inspect erosion / stormwater controls during	MO	4	\$ 5,000	\$ 20,000	
4	Stormwater Maintenance	MO	4	\$ 27,300	\$ 109,200	
5	Silt Fence non-reinforced	LF	3,000	\$ 4.27	\$ 12,810	
6	Silt Fence removal and disposal	LF	3,000	\$ 3.37	\$ 10,110	
7	6-inch over-excavation (17 acres)	CY	13,709	\$ 6.50	\$ 89,109	Excavate, load, haul and place in NAP
8	Embankment removal	CY	80,000	\$ 25.00	\$ 2,000,000	Partial removal and elimination from Dam Safety program
9	Site stabilization	Ac	17	\$ 3,500.00	\$ 59,500	
10	Closure sign	Ea	1	\$ 125	\$ 125	
11	Contingency	%	2,410,854	10%	\$ 241,085	
12	3rd party certification survey	Ac	17	\$ 4,500	\$ 76,500	
13	Construction QA/QC oversight	LS	1	\$ 93,500	\$ 93,500	
14	Closure certification report	LS	1	\$ 8,000	\$ 8,000	
15	Groundwater Monitoring	Ls	1	\$ 98,678	\$ 98,678	Minimum remaining sampling events to demonstrate closure
	Total				\$ 2,928,617	

Notes: 1. Estimate based on starting with current condition as of September 14, 2018 to achieve clean closure condition

Established in 1960, Golder Associates is a global, employee-owned organization that helps clients find sustainable solutions to the challenges of finite resources, energy and water supply and management, waste management, urbanization, and climate change. We provide a wide range of independent consulting, design, and construction services in our specialist areas of earth, environment, and energy. By building strong relationships and meeting the needs of clients, our people have created one of the most trusted professional services organizations in the world.

Africa	+ 27 11 254 4800
Asia	+ 852 2562 3658
Australasia	+ 61 3 8862 3500
Europe	+ 356 21 42 30 20
North America	+ 1 800 275 3281
South America	+ 56 2 2616 2000

solutions@golder.com
www.golder.com

Golder Associates Inc.
2108 W. Laburnum Avenue, Suite 200
Richmond, VA 23227 USA
Tel: (804) 358-7900
Fax: (804) 358-2900



Engineering Earth's Development, Preserving Earth's Integrity

Golder, Golder Associates and the GA globe design are trademarks of Golder Associates Corporation
